




PROJECT: ERDC Site Wide Monitoring Plan (13 002-4)	BORING ID: KAR13-015 (Completed)		
	LOCATION: Keno Hills Silver District (KHSD)		
	DRILLING CONTRACTOR: Access Consulting Group	NORTHING: 7086547.66	EASTING: 474890.37
	DRILLING EQUIPMENT: Midnight Sun Drilling Inc.	GROUND SURFACE ELEV. (masl): 817.19	TOC ELEVATION (m ags): 0.74
	DRILLING METHOD: Air Rotary	TOTAL DEPTH (m): 49.68	WATER DEPTH (m TOC): 6.88
LOGGED BY: KR/MR	SAMPLING METHOD: 2 Feet (0.61 m) Continuous Sampling	DATE STARTED: September 8, 2013	DATE COMPLETED: September 9, 2013

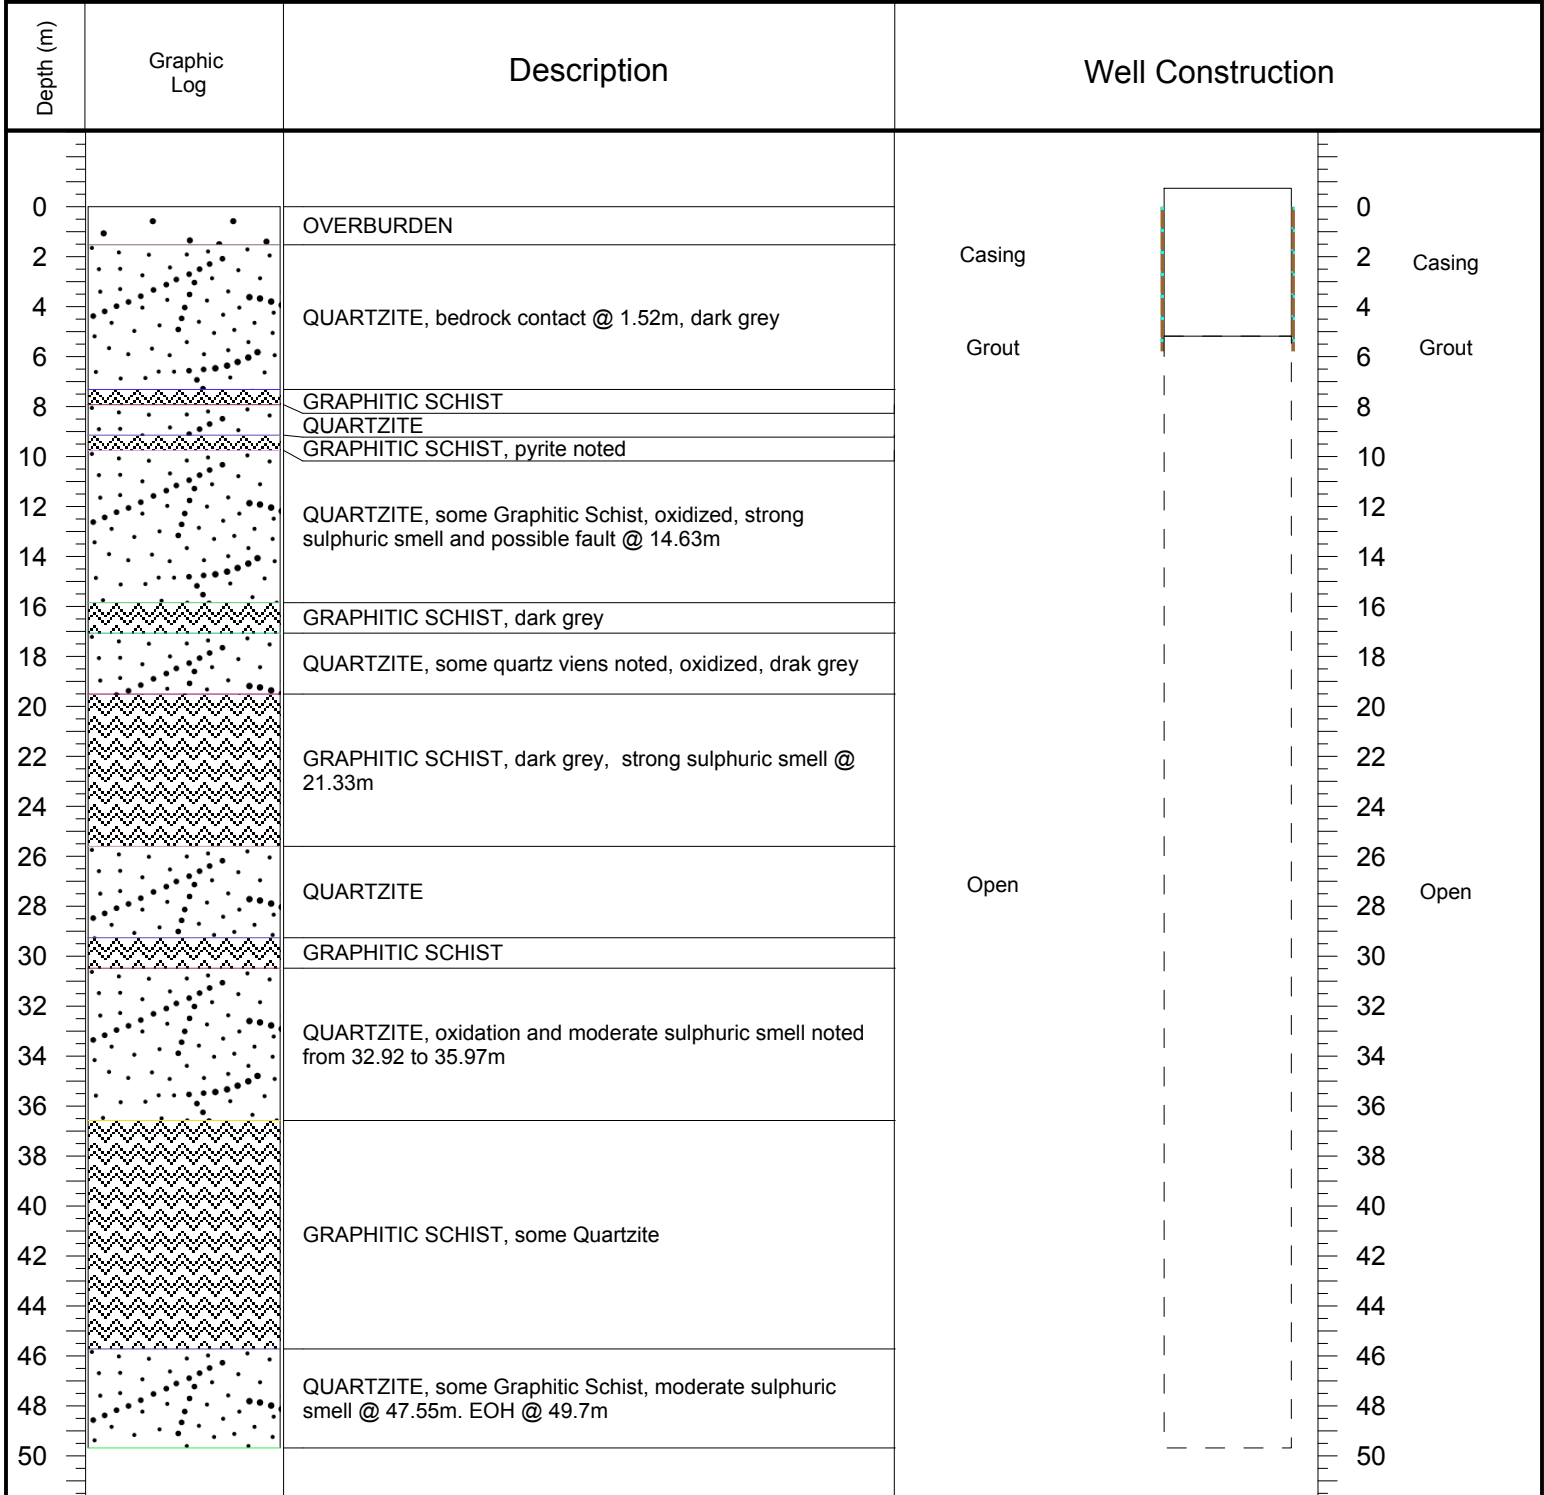

NOTES: Well is 6 inches in diameter (ID). Grouted into bedrock, and open below. Well was developed and capped. Casing to 5.18m bgs. EOH @ 49.68m.
