

EXTRA COPY


COLUMBIA GAS DEVELOPMENT OF CANADA LTD.

FINAL WELL REPORT


FOR

COLUMBIA ET AL KOTANEELEE YT I-48A

Prepared By:

  
\_\_\_\_\_  
J.A. Anderson  
Drilling Engineer

Approved By:

 91-10-09  
\_\_\_\_\_  
B.M. Jackson  
Chief Drilling and Production Engineer

October 1991

NATIONAL ENERGY BOARD  
ENGINEERING BRANCH  
OCT 18 1991

Columbia et al Kotaneelee YT I-48A

Table Of Contents

Section A

- Introduction
- Operations Summary
- Locality Map

Section B

General Data

Section C

Geological Summary

Section D

Logging Summary

Section E

- Drilling Summary
- Depth vs Days
- Time Breakdown
- Bit Record
- Casing Report
- Cementing Report
- Drilling Fluid Summary
- Well Control
- Leak Off Testing
- Fishing
- Deviation Survey

Section F

- Completion Summary
- Well Schematic
- Tubing Summary
- Perforation Record
- Stimulation
- Production Testing Summary
- Gas Analyses

Enclosures

IDF Drilling Fluid Summary  
Sperry Sun Directional Drilling Summary  
Northland Production Test Field Data  
Datalog Hydrocarbon Well Log  
Schlumberger Open Hole Logs  
Schlumberger Cased Hole Logs  
Schlumberger Production Log

## SECTION A - INTRODUCTION

### OPERATIONS SUMMARY

#### COLUMBIA ET AL KOTANEELEE YT I-48A

A workover of the Columbia et al Kotaneelee YT I-48 well in 1990 and 1991 showed the lower portion of the production casing to be unsuitable for production use. Excessive channelling of the production casing cement job in 1980 left the production casing without hydraulic isolation over the Nahanni pay interval. Extreme corrosion in combination with parted casing at 3600m deemed future workover operations impractical.

The YT I-48 well was abandoned by setting a 5.65m<sup>3</sup> thermal cement plug from PBD of 3753m to 3400m. With 0.62m<sup>3</sup> of cement in the formation, a squeeze pressure of 8 MPa was maintained. A bridge plug was set at 3331m and pressure tested to 12 MPa. A whipstock packer was set at 3283m with the top of the whipstock at 3274m. The abandonment of Columbia et al Kotaneelee YT I-48 was complete.

Drilling operations commenced at Columbia et al Kotaneelee YT I-48A with the milling of the whipstock lug. A window was milled in the 177.8mm casing from 3273.70-3280.9m. A 152.4mm hole was directionally drilled from 3281m in the Besa River to 3915m, 68m into the Headless formation. The well was logged and a 127mm production liner run from 3915-2886m and cemented full length.


The production liner was cleaned out to PBD of 3900m. The casing was displaced to inhibited water and cement bond logs run. The bond logs showed excellent bonding across the Nahanni pay zone and good isolation over the liner lap. A production packer was set at 3642m and 89mm tubing was run to surface. The wellhead was installed and all surface and downhole equipment pressure tested. The well was then perforated with through tubing perforating guns. A total of 135m was perforated over the gross interval 3658-3889m. The well was flowed on cleanup for 72 hours at which time a 56.6m<sup>3</sup> acid wash/squeeze was performed. The well was flowed on cleanup after the acid wash at 968.5 x 10<sup>3</sup>m<sup>3</sup>/d at 20,700 kPa (34.4 MMCF at 3000 psi). The drilling rig and support equipment was moved out and Columbia et al Kotaneelee YT I-48A was turned over to production operations 91-07-22. The well was put on production 91-07-25 and preliminary results indicate the well is capable of producing in excess of 1268 x 10<sup>3</sup>m<sup>3</sup>/d (45 MMCFD).

ii) LOCALITY MAP

# COLUMBIA et al KOTANEELEE "YT 1-48A"

AMOCO BEAVER  
COLUMBIA KOTANEELEE  
PAN-AM KOTANEELEE  
CANADA SOUTHERN BEAVER

YT G-01  
YT B-38  
YT A-1  
YT I-27

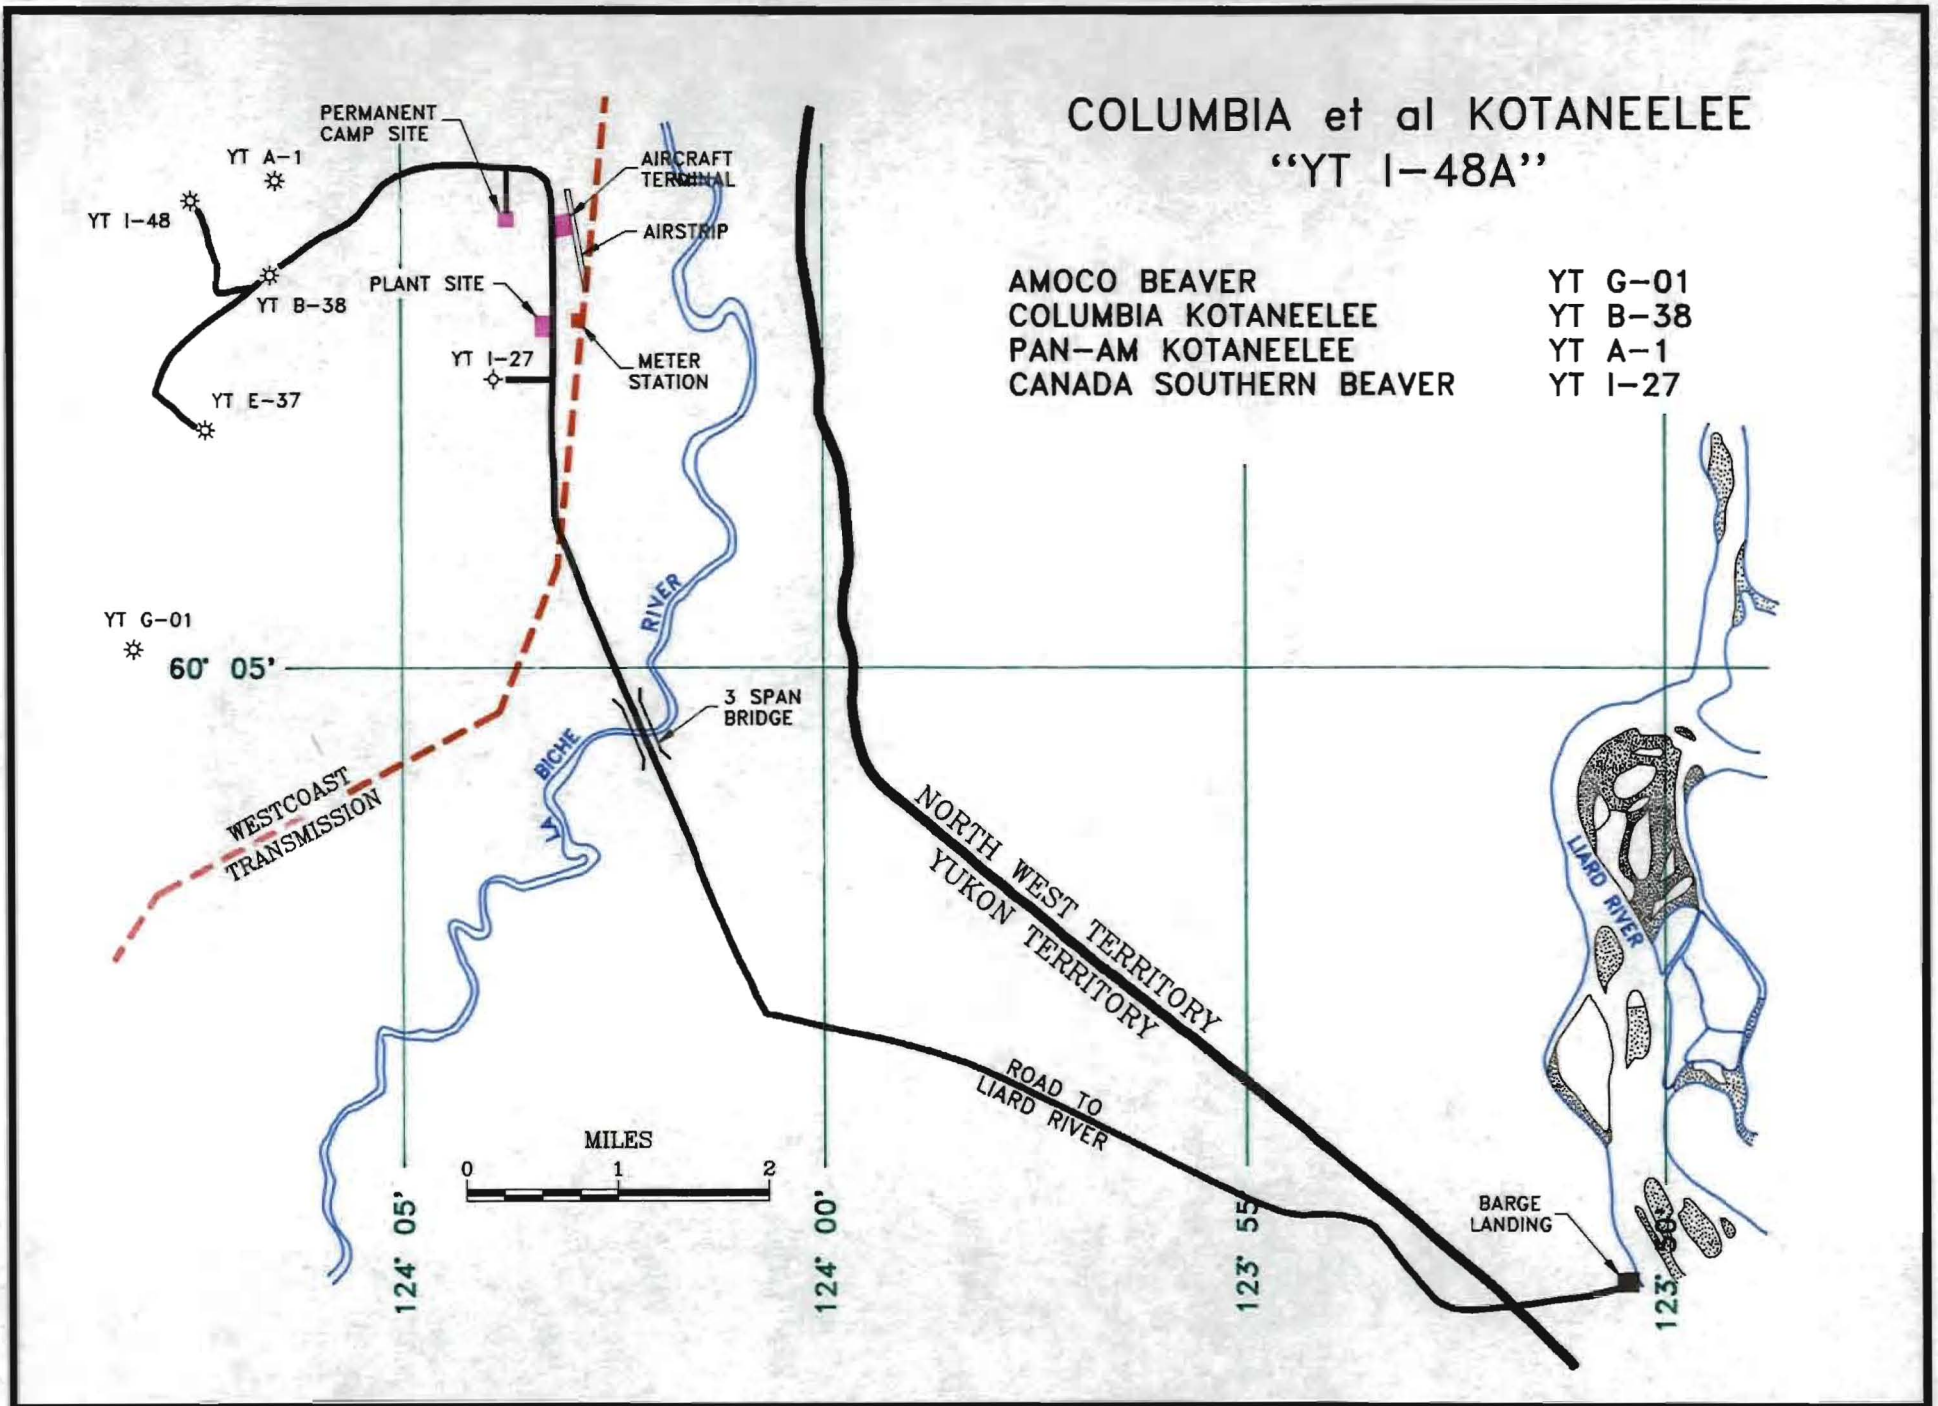

**B. GENERAL DATA**

**WELL NAME AND NUMBER:** Columbia et al Kotaneelee Y.T. I-48A  
**ADW NUMBER:** 1425

**WELL LOCATION:** Yukon Territory Unit I Section 48  
Latitude: 60°07'35.917"  
Longitude: 124°07'36.45"  
Universal Well Location Reference:  
Latitude: 60.12664  
Longitude: 124.12679

**UNIQUE WELL IDENTIFIER:** 300I486010124001

**OPERATOR:** Columbia Gas Development Of Canada Ltd.  
#1000, 639-5th Ave. S.W.  
Calgary, Alta  
T2P 0M9

**DRILLING CONTRACTOR:** Kenting Hi-Tower Drilling  
P.O. Box 6650  
Postal Station "D"  
Calgary, Alta Canada  
T2P 2V8

**DRILLING UNIT:** Kenting Hi-Tower Rig No. 7  
Oilwell Model 66

**WELL INFORMATION:**

Ground Level Elevation:	827.34 m
K.B. Elevation:	832.70 m
Distance "H":	4.10 m
Ground to K.B.:	5.36 m
PBTD.:	3900 mKB
Total Depth:	3915 mKB
Sidetrack Initiated:	1991-05-19 @ 02:15 hr.
Drilling Commenced:	1991-05-24 @ 13:30 hr.
Rig Released:	1991-07-18 at 11:00 hr.
Casing Window:	3274 - 3280 mKB
Open Hole:	152.4mm from 3280-3915m KB
Drilling Authority:	D.A. 1425
Classification:	Development Well

**PARTICIPATION:**

(OP) Columbia Gas Development Of Canada Ltd.	33.15625%
Amoco Canada Resources Ltd.	31.21875%
Amoco Canada Petroleum Ltd.	18.75000%
Esso Resources Canada Limited	15.00000%
Mobil Oil Canada Ltd.	1.87500%

**INTERMEDIATE CASING:**

177.8 mm, 47.6 kg/m, MN-80, 8rd, LT&C, SS casing  
from 3280 - 2591 mKB and

177.8 mm, 43.2 kg/m, MN-80, 8rd, LT&C, SS casing  
from 2591-1118 mKB and

177.8 mm, 47.6 kg/m, L-80, 8rd, LT&C, SS casing  
from 1118 m to surface.

.The casing is cemented to surface.

**PRODUCTION LINER:**

127 mm, 26.8 kg/m, L-80 Hydril SFJP, SS casing  
from 3914.5 - 2885.9 mKB.

Liner cemented with 2.3 tonnes Thermal 3F 1300 kg/m<sup>3</sup>  
scavenger slurry containing 0.80% CMHEC (fluid loss control  
additive) + 1.00% T-10 (cement dispersant) + 0.60% R-55  
(retarder) + 14.0 tonnes Thermal 3F mixed to a density of 1877  
kg/m<sup>3</sup> containing 0.80% CMHEC + 1.00% T-10 + 0.60% R-55.  
Cement top at 2886m KB

#### WELLHEAD (FMC):

279.4 mm, 34500 kPa x 179.4 mm, 79000 kPa tubing spool complete with 46 mm, 79000 Kpa SSO's and 46 mm x 79000 kPa WKM gate valve.

179.4 mm, 79000 kPa x 77.8 mm, 79000 kPa tubing head adapter complete with 89 mm CS Hydril thread and test port.

Two (2), 77.8 mm x 79000 kPa WKM master valves. (NACE trim).

One (1) studed cross (79000 kPa x 77.8 mm) with three (3) 76.2 mm x 34500 kPa SSO's.

One (1) 76.2 mm x 34500 kPa wing valve. (NACE trim) c/w 76.2 mm, 34500 kPa x 76.2 mm LP companion flange.

One (1) bottom hole test adapter, 76.2 mm, 34500 kPa x 89 mm EUE lift thread, metal lip seal, needle valve and gauge.

#### SIDETRACKED HOLE:

The I48A well was sidetracked out of the 177.8mm production casing of the I48 well at 3273m utilizing a whipstock packer. Cement bond logs indicated adequate hydraulic isolation was provided in the 177.8mm casing/216mm hole and 177.8mm casing/244.5mm casing annulus from 3291m KB to surface. The presence of cement above and below the kick off point was necessary in order to minimize mechanical and well control problems. The small length of section between the 177.8mm cementing stage tool and the 244.5mm intermediate casing necessitated the use of a whipstock packer rather than conventional section milling. Although milling operations were more time consuming than anticipated, the whipstock packer provided a positive and rapid exit from the old wellbore and the sidetrack was considered an operational success.

## C. GEOLOGICAL SUMMARY

### HORN RIVER

3281-3657m

The Horn River consisted of dark grey to grey black fissile shale. It was micromicaeous in part with common disseminated and nodular pyrite. At the bottom of the formation the shale became interbedded with a white to light grey, very fine to fine crystalline, dolomitic limestone.

The total gas readings over this formation ranged between 30 and 70 units of methane with trace ethane. There were no significant gas responses over this interval.

### NAHANNI

3657-3847m

The Nahanni formation consisted primarily of dolomite with interbedded limestone. The dolomite was either light grey, very fine crystalline, dense, and tight, or medium to dark grey, fine crystalline, and tight. Most of the fracturing seemed to originate in the light grey dolomite as well as the better gas shows. At 3629 the penetration rate picked up from around 40 min/meter to around 20 min/meter. At this point the dolomite became less dense and hard.

The total background gas readings over this formation were between 30 and 90 units. The gas consisted of methane and traces of ethane. There were several good shows due to fractures over this formation:

3674.4-3677.0	180u/40u
3688.0-3693.0	189u/30u
3702.0-3703.0	176u/44u
3705.0-3706.0	251u/51u
3715.0-3716.0	114u/44u
3720.0-3729.0	914u peak at 3724m 200-300u average over rest of show /50u
3736.0-3742.0	377u peak at 3739m 100-120u average over rest of show /30u
3751.0-3754.0	173u/20u
3766.0-3772.0	358u peak at 3768m 100-200u average over rest of show /40u
3817.6-3825.0	517u peak at 3818m 200u average over rest of show /100u
3833.2-3836.6	340u/100u

It should be noted that the density of the mud was 15 to 20 points higher than the estimated formation pressures so that overbalancing occurred and may have masked some potential gas shows.

### HEADLESS

3847-3920m

The Headless formation consisted of the same dolomite and limestone as the Nahanni but it becomes increasingly argillaceous and silty. The background gas readings over this interval were around 100 units of

methane with trace ethane. There were a few gas responses over this interval:

3859.0-3866.0	382u/100u
3866.2-3867.4	308u/50u
3875.0-3892.0	3789u peak at 3883m
	Note: gain 1 cubic meter in vol.
	200u average over rest of show/50u
3904.0-3905.0	247u/90u

According to the gas shows there is at least 80 meters of potential pay over the Nahanni and Headless formations. Once again it should be noted that the mud weight was quite high and could have masked potential gas shows.

D. LOGGING SUMMARY

OPEN HOLE LOGS:

Run #1: Phasor Induction-SFL-SP-GR in combination with  
Borehole Compensated Sonic-GR-CAL. Logged from  
3915-3274m KB. Log date: 25-June-1991.

Run #2: Formation Microscanner (FMS)-GR-CAL. Logged from  
3913-3600m KB. Log date: 25-June-1991.

\*TVD logs were prepared for each of the above logs.

CASED HOLE LOGS:

Completion Record: - 177.8mm bridge plug set at 3331.0m wireline KB.  
- 177.8mm whipstock packer set at 3271.4m wireline  
KB. Log date: 17-May-1991

Compensated Bond-Variable Density-Cement Evaluation Log-GR-CCL.  
Logged from 3900-2880m KB. Log date: 01-July-1991. Cement Advisor  
(Processed Log) Log date: 01-July-1991.

Completion Record: Setting of 127mm production packer c/w tailpipe  
assembly at 3642m KB. Log date: 04-July-1991.  
Summary of Perforating Operations. Log date:  
11-July-1991.

PRODUCTION LOGS:


Production Logging Tool - Flow Analysis c/w Spinner Tool, Pressure and  
Temperature Recorder and Gradiomanometer Tool. Logged from  
3880-3600m KB. Log run prior to stimulation. Log date: 15-July-1991.

NOTE: All logs run by Schlumberger.

E. DRILLING SUMMARY

# COLUMBIA ET AL KOTANEELEE YT 148A

## DEPTH vs DAYS

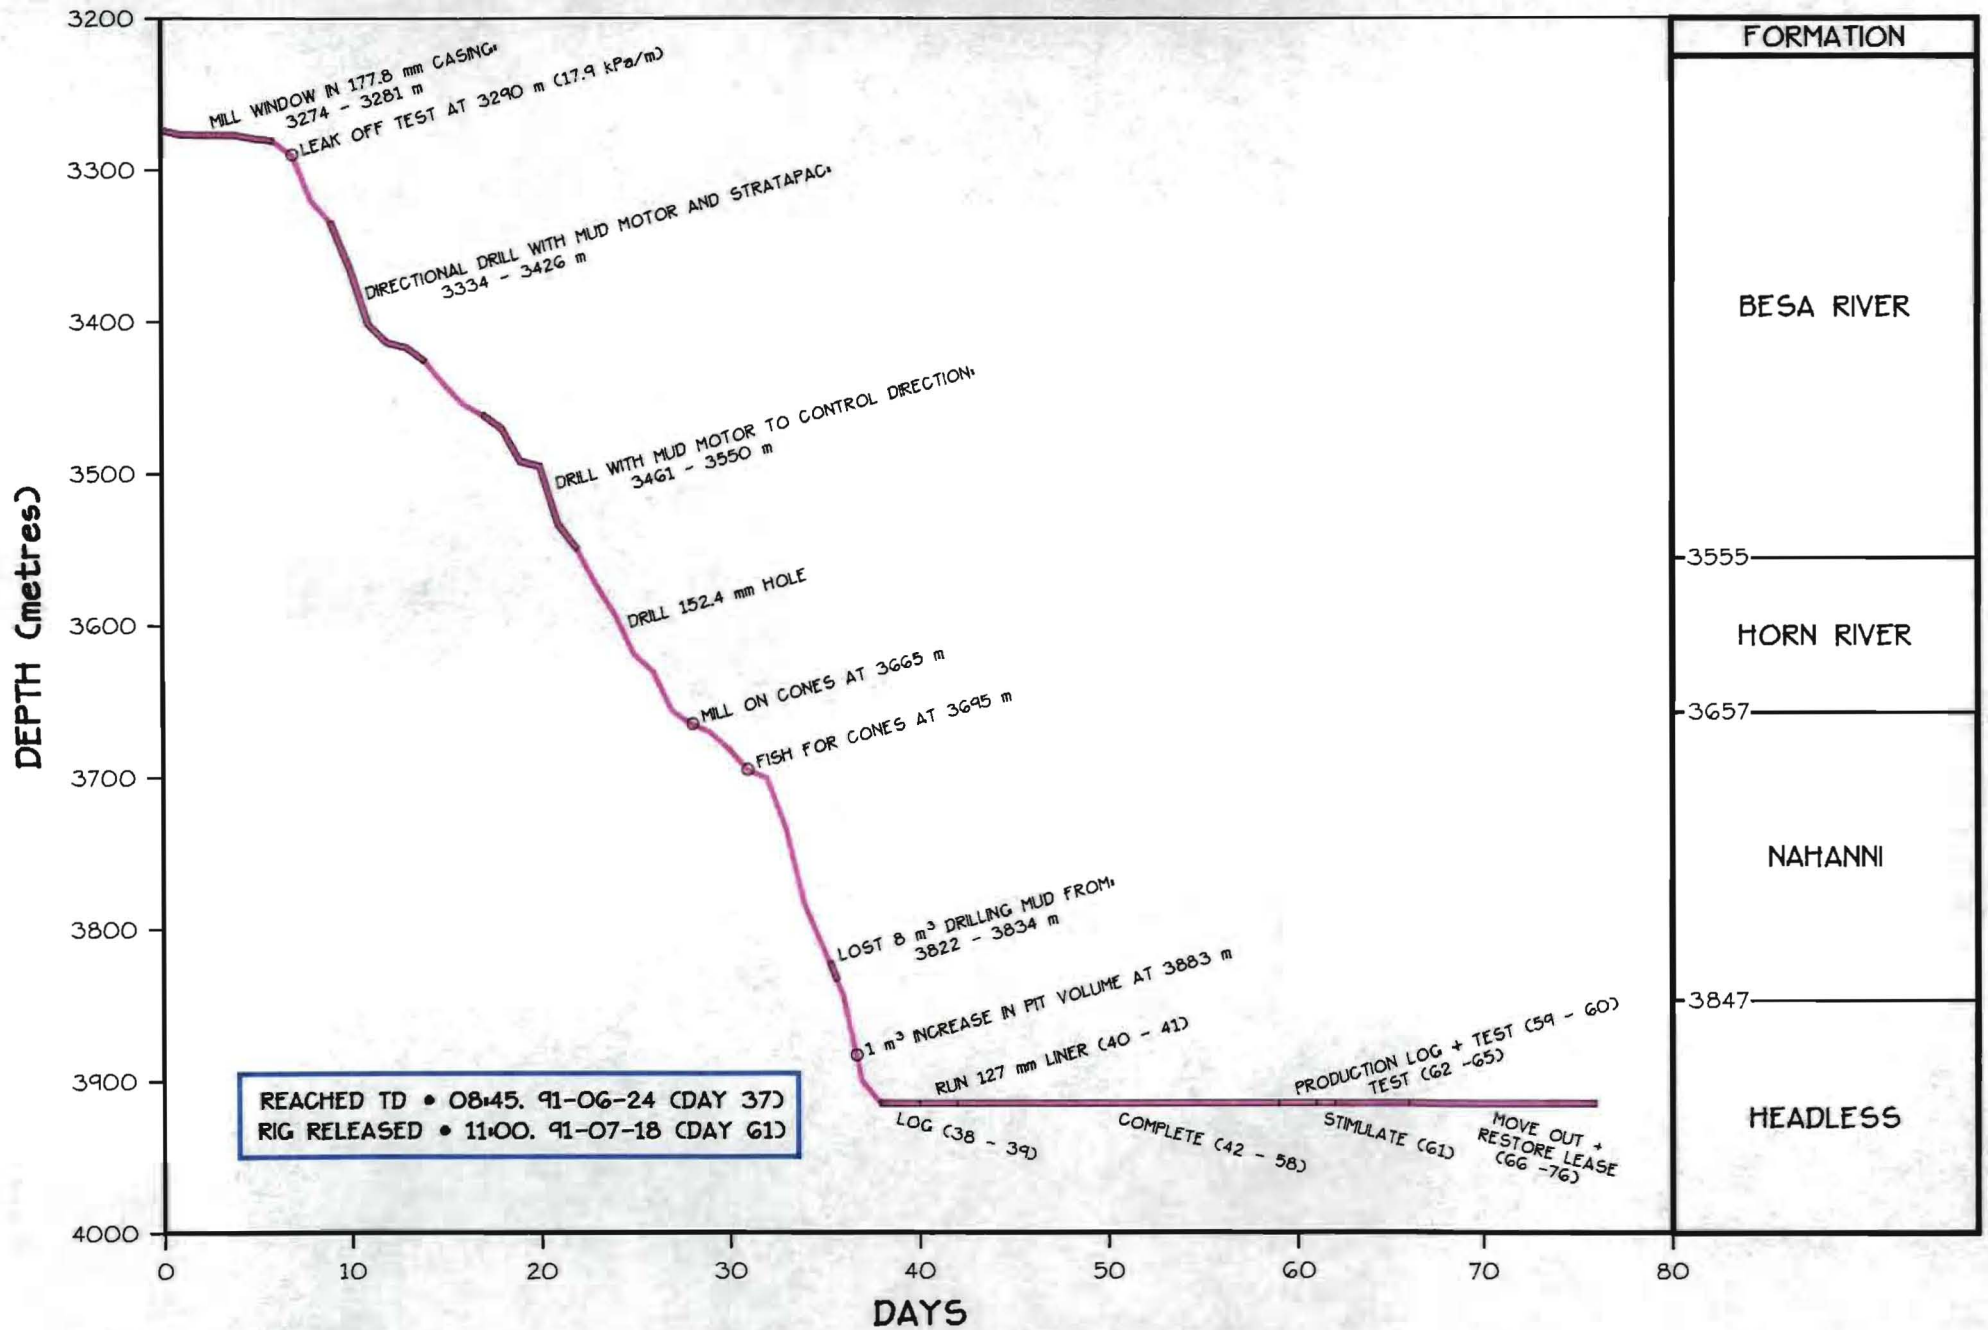


COLUMBIA ET AL KOTANEELEE Y.T. I-48A

Time breakdown from the initial running in the hole of the whipstock at 06:00 hrs, 91-05-18 to rig release at 11:00 hrs, 91-07-18.

<u>Operation</u>	<u>Hours</u>	<u>Operation</u>	<u>Hours</u>
Drilling	366.5	Lay down drill string	22.5
Tripping	355.75	Tear out BOP's, Install Wellhead	21
Testing Handling Tools, Rigging Up, Pressure Testing etc.	115.75	Slip & cut	19.5
Waiting On Approvals, Orders, Equipment etc.	81.25	Ream	14.75
Circulating	80.75	Mix Mud	14.25
Milling	54.75	Clean Mud Tanks	12
Logging	43	Other	12.25
WOC	37.5	Run Casing	11
Perforating	32.25	Rig Repair	7.5
Rig Service	30	Polish Off/Drill Out Liner	7
Clean Up Tools And Lease, Load Out Equipment	29.5	Cementing	3
Survey	26.5	Stimulation	2.25
	24	Leak Off Test	1.75
		<b>TOTAL</b>	<b>1426.25</b>

COLUMBIA ET AL KOTANEELEE YT 148A

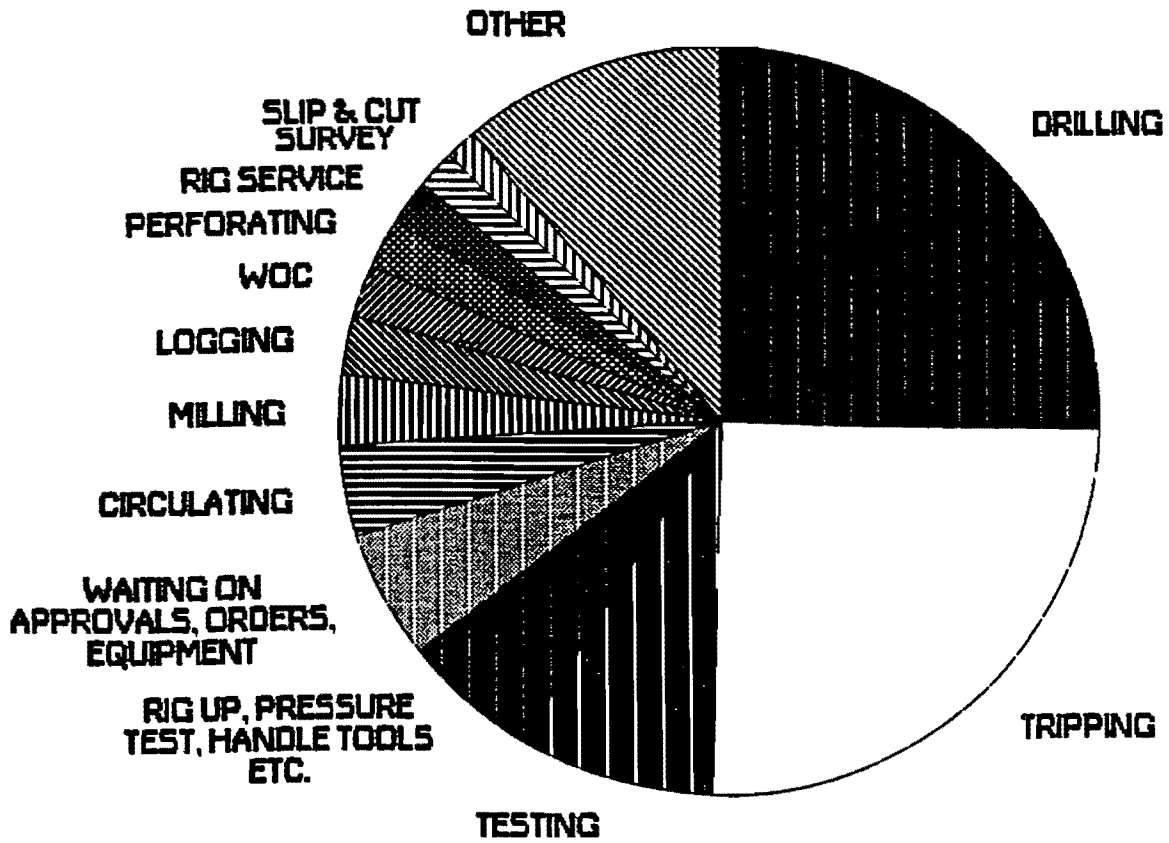

COLUMBIA GAS DEVELOPMENT OF CANADA LTD.



BIT RECORD

WELL NAME Columbia et al Kotaneelee Y.T. I-48A

BIT No.	SIZE	SERIAL NUMBER	TYPE	JETS (mm)	IN	OUT	METERS DRILLED	HOURS	T-B-G	FORCE	RPM
1	152.4	72040	R7	3x12.7	3277.3	3277.3	Attempt to exit window				
2	152.4	PR680	J33	3x12.7	3280	3334	54	25	6-5-I	10	70
3	152.4	1102B	KDM33	3x22.2	3334	3402	68	31 1/4	5% wear	3-4	200
RR3	152.4	1102B	KDM33	3x22.2	3402	3414	12	4 3/4	very good	3-4	200
RR3	152.4	1102B	KDM33	3x22.2	3414	3426	12	15	worn out	3-4	200
4	152.4	H-69605	HP62	3x20	3426	3441	15	13 1/4	2-8-I	3-5	150
5	152.4	P5295	J33	3x20	3441	3455	14	13 1/2	2-8-I	3-4	150
6	152.4	211K03	R4	3x20	3455	3461	6	6	3-3-I	8	65
7	152.4	1254	KDM44	3x20	3 61	3495	34	33 1/2	40% wear	1-5	75
8	152.4	TW2968	HP53	3x20	3495	3550	55	23 1/4	2-3-I	5	80
9	152.4	PH6315	HP53	3x15.9	3550	3593	43	29 1/2	4-3-I	10	65
10	152.4	TW2947	HP53	3x10.3	3593	3630	37	30	4-1-I	10	50
11	152.4	215999	S88F	3x10.3	3630	3664.5	34.5	19 3/4	Lost cones	10	45/50
	152.4	Flat Bottom Mill						4 1/2		12-15	45
12	152.4	PL603	J55	3x14.3	3664.5	3667	2.5	2 3/4	8-2-I	11	45
13	152.4	28176	J55	3x14.3	3667	3672	5	3 1/2	3-6-I	10	45
14	152.4	526-PA	J55	3x14.3	3672	3681	9	6	4-1-I	8-10	45
15	152.4	433-VI	J55	3x14.3	3681	3695	14	11 1/2	8-8-I	7-9	45
16	152.4	990SF	J55	3x14.3	3695	3733	38	17 1/2	7-3-I	10	45
17	152.4	137UL	J55	3x14.3	3733	3784	51	20 3/4	1-4-I	7-8	45
18	152.4	232NK	J55	3x15.9	3784	3843	59	24 3/4	3-3-I	10	45
19	152.4	140 VL	J55	3x15.9	3843	3915	72	27 1/4	4-4-I	10	
20	152.4	D98EF	J4	3x15.9	CLEAN OUT TO TOP OF LINER						
21	105.5	C10916	Klustrite Mill		to drill out pack off bushing and clean out.						

Motor  
Motor  
Motor  
Motor



# COLUMBIA GAS DEVELOPMENT OF CANADA LTD.

## CEMENTING REPORT

WELL NAME Columbia et al Kotaneelee YT I-48A DATE June 27/91  
REFLUSHED WITH: 10 m<sup>3</sup> OF water  
AVERAGE RATE OF .5 m<sup>3</sup>/m CEMENTED BY: Nowasco  
STAGE #1 2.3 tonnes Thermo 3 + .8% CMHEC + 1.0% T10 + .6% R-55 slurry wt.  
1300 kg/m<sup>3</sup> (scavenger cement)

STARTED TO MIX CEMENT AT 11:41 (AM, PM) FINISHED MIXING CEMENT AT 11:49 (AM, PM)  
TOTAL SLURRY MIXED 5 m<sup>3</sup> MAXIMUM PUMPING PRESSURE 12000 kPa  
STAGE #2 14 tonne Thermo 3 + .8% CMHEC + 1.0% T10 + .6% R-55 slurry wt.  
1877 kg/m<sup>3</sup> tail in cement.

STARTED TO MIX CEMENT AT 11:49 (AM, PM) FINISHED MIXING CEMENT AT 12:15 (AM, PM)  
TOTAL SLURRY MIXED 10.9 m<sup>3</sup> MAXIMUM PUMPING PRESSURE 12000 kPa  
PLUG DOWN AT 1331 (AM, PM) DATE: June 27/91 BUMP PLUG WITH 26000 kPa  
PLUGS HOLDING yes IF NOT, PRESSURE HELD ON PLUG \_\_\_\_\_ kPa FOR \_\_\_\_\_ HRS.  
PUMPED PLUG 3905 m WITH 19.2 m<sup>3</sup> OF drill mud VOLUME TO FLOAT COLLAR 19.2 m<sup>3</sup>  
SLURRY DENSITY 1887 kg/m<sup>3</sup> AVERAGE DISPLACEMENT RATE: 0.5/0.15 m<sup>3</sup>/m  
TEMPERATURE: CEMENT 14 °C WATER 13 °C SLURRY 17 °C  
CULATED \_\_\_\_\_ m<sup>3</sup> OF CEMENT BACKWASHED 2.7 m<sup>3</sup> OF CEMENT. scavenger  
NO. OF SAMPLES TAKEN 6 WITNESSED BY: Ed Prohl FOR CONTRACTOR.  
R. Toole/J. Anderson FOR COLUMBIA  
SURPLUS: none

TRANSFER NO. \_\_\_\_\_  
REMARKS: Good cement job. Did not lose any fluids to formation during cement job. Displaced last 4.1m<sup>3</sup> of Thermal 3F in plug flow of 0.15m<sup>3</sup>/min Preflush water and scavenger slurry displaced past pay zone in turbulent flow.



INTERNATIONAL DRILLING FLUIDS CORPORATION  
#300, 300 - 5th AVENUE S.W.  
CALGARY, ALBERTA, CANADA T2P 3C4  
TELEPHONE: (403) 266-0722  
FAX: (403) 237-8331

**WELL SUMMARY**  
**FOR**  
**COLUMBIA GAS DEVELOPMENT OF CANADA**  
**COLUMBIA ET AL KOTANEELEE YT-I-48**

## COLUMBIA GAS DEVELOPMENT OF CANADA

### COLUMBIA ET AL KOTANEELEE YT-I-48

#### DISCUSSION BY INTERVALS

**HOLE SIZE:** 178mm CASING

**MUD TYPE:** GEL/CHEMICAL (Weighted)

Mixed 90m<sup>3</sup> of kill mud at 1200kg/m<sup>3</sup>. Displaced the hole to mud and built volume increasing the yeild point to a level high enough to suspend the Barite. The possibility of H<sub>2</sub>S required raising and controlling the pH at 11.0 with Caustic Soda. Also pre-treated with 1.6kg/m<sup>3</sup> of Sulban (H<sub>2</sub>S Scavenger). Mixed a Barite pill prior to each trip (45 sacks) which continued to increase the density. Controlled the density at 1200kg/m<sup>3</sup> with water dilution at 20/L min. when circulating. Due to the high bottom hole temperature of approximately 350°F the viscosity at the shaker was 20 to 40 sec/L higher than at the suction. Set a bridge plug at 3331 metres. Whipstock packer at 3277 metres, logged and ran in with mill. Milled a window in the 178mm casing. Kicked off and drilled 152mm hole to 3290 metres.

**HOLE SIZE:** 152mm

**MUD TYPE:** POLYMER (Weighted)

Pre-mixed a weighted Polymer system on May 25, 1991. Displaced the hole over to the Polymer system and built volume and condition the mud. Drilled ahead, mixing 1 jug of X-Cide and 3 pails PTS-200 daily to prevent the Polymers from breaking down due to the high bottom hole temperature (350°F+). Maintained the viscosity at 35-45 s/L using IDVIS D and ASP-721. Controlled pH at 10.5 using Caustic Soda. The Yield point was 10 (Pa) until 3435 metres and then started to climb to 14. Increased H<sub>2</sub>O additions and added 27 sacks IDF FCL to lower the yield point. ASP-721 additions were stopped on June 8th at 3530 metres and resumed on June 17th at 3680. The fluid loss climbed from 10mL to 37mL. Used Drispac S. Lo and IDF-FLR to control the filtrate. Fluid loss was very unstable until additions of Flo Plex (3.7kg/m<sup>3</sup>) at 3800 metres. Fluid loss dropped below 8mL.

While drilling from 3784 metres - 3822 metres, the hole took approximately 8m<sup>3</sup> fluid. Prior to a trip out with Bit #17, a 14m<sup>3</sup> L.C.M. pill was spotted in the annulus. No further losses were encountered while drilling. TD was 3915 metres. Logged and ran 127mm liner. Lost approximately 21m<sup>3</sup> while running liner. Pumped L.C.M. and by passed shaker screens while circulating prior to cementing.

**COLUMBIA GAS DEVELOPMENT OF CANADA**  
**COLUMBIA ET AL KOTANEELEE YT-I-48**

**CONCLUSIONS AND RECOMMENDATIONS**

**HOLE SIZE: 178mm CASING**

**MUD TYPE: GEL/CHEMICAL (Weighted)**

Pre-mixed a weighted Gel system prior to drilling out the bridge plug. The density was raised to 1200kg/m<sup>3</sup> due to expected gas pressures. Maintained the pH at 10.5-11.0 and pre-treated with .6kg/m<sup>3</sup> Sulban due to the possibility of H<sub>2</sub>S. This mud system was used to cut a window in the casing at 3273 metres with no problems.

**HOLE SIZE: 152mm**

**MUD TYPE: POLYMER**

Pre-mixed and displaced the hole with a weighted Polymer system after the window was cut in the casing. The Polymer system was used to prevent any damage to the producing formation. The density was controlled in the 1180-1210kg/m<sup>3</sup> range due to the possibility of high formation pressures. The hole was directionally drilled to stay away from the old hole. Fished for cones at 3664 metres and 3695 metres. The hole was in good shape and no problems were encountered other than the difficulty keeping the fluid loss down. Flo Plex was added to lower fluid loss below 12mL and no further problems were reported.

**COLUMBIA GAS DEVELOPMENT OF CANADA**

**COLUMBIA ET AL KOTANEELEE YT-I-48**

**PROGRAMMED PRODUCT COST DISCUSSION**

Programmed Product Cost	\$ 82,380.00
Actual Cost	\$ 145,118.30

**PRODUCT COST SUMMARY vs PROGRAMMED COST**

Product	Programmed Usage	Actual Usage	Cost Difference	Reason For Use
Bentonite	200	390	\$ 1,900.00	viscosity
Barite	1800	3889	26,112.50	density
Bicarbonate	50	5	(1,800.00)	cement contamination
Caustic Soda	42	74	960.00	pH control
IDBOND (ASP 721)	50	56	810.00	shale control
IDF FCL	40	10	(960.00)	thinner
Soda Ash	5	40	700.00	water hardness control
X-Cide 207	20	40	2,800.00	Biocide
IDF-FLR (Drispac)	60	101	6,560.00	fluid loss
DFLC	30	31	178.00	thinner
IDVIS D	25	40	6,300.00	viscosity
PTS 200	80	69	(2,860.00)	temperature stability
Mica	--	20	317.80	LCM
Sulban	--	20	5,000.00	H <sub>2</sub> S Scavenger
Sawdust	--	188	940.00	LCM
Lime	--	20	171.60	camp use
Kwik-Seal	--	56	1,950.00	LCM
Sodium Sulphite	--	30	1,470.00	polymer stability
DEFOAMER	--	19	2,850.00	gas entrapment
Glass Beads	--	36	2,880.00	torque reducer
VISPLEX	--	1	225.00	viscosity
FLOPLEX	--	21	2,625.00	fluid loss
Celloflake	--	40	924.00	LCM

## COLUMBIA GAS DEVELOPMENT OF CANADA

### COLUMBIA ET AL KOTANEELEE YT-I-48

#### PRODUCT USE DISCUSSION

##### WORKOVER

The product cost for the workover section of the re-entry was \$15,000.00 over our estimated program cost. This overrun was due to the time spent on this section (estimated 4 days, actual 26 days) and the Barite used for trip pills during this time (\$12,000.00). Extra Bentonite, Caustic Soda and four pails of Sulban accounted for the balance of the cost in excess of the estimate.

##### RE-DRILL

The re-drill section of the project was accomplished within the programmed time frame, but the product cost was \$47,500.00 above the programmed estimate. Barite use was again the biggest reason as about \$14,000.00 over the programmed estimate was used. Trip pills and lost circulation accounted for the use. The centrifuge was used to reduce the density as it climbed above levels required for pressure control due to the many trip pills used.

Fluid loss control was the only drilling fluid problem experienced on this well. The programmed combination of IDF-FLR, Drispac, PTS 200 and Sodium Sulphite could not stabilize the fluid loss once bottom hole temperatures climbed to the expected high levels. FLOPLEX was brought to location and used to stabilize the fluid loss. Fluid loss control contributed to \$7,800.00 of the cost over programmed estimate.

Lost circulation while drilling and running liner accounted for \$4,200.00 of lost circulation material and losses of \$7,200.00 of mud. The mud was on standby in a premix tank on location, but the cost to build the additional volume had not been included in our estimate.

Glass Beads were used to reduce torque between the casing and drillstring when kicking off (\$2,880.00). Scavenger to control hydrogen sulphide (\$5,000.00), Biocide to ensure bacteria did not become a problem (\$2,800.00 above estimate) and DEFOAMER to reduce gas entrapment (\$2,850.00) accounted for the balance of the cost over programmed estimate.

## COLUMBIA GAS DEVELOPMENT OF CANADA

### COLUMBIA ET AL KOTANEELEE YT-I-48

#### FUTURE AREA WELLS or RE-ENTRIES

#### PROGRAM RECOMMENDATIONS

1. The Polymer system is the best system to use on main hole or on a re-entry section in this area. It provides shale stability if these sections are in open hole, does not flocculate due to the high bottom hole temperatures and provides even cleaning ability through the different annular sizes. In addition, it appears that no formation damage was done as the well cleaned up and is producing as expected.
2. Programs for fluid loss control in the area will have to include product equivalent to FLOPLEX in the Polymer system. Conventional fluid loss polymers along with polymer stabilizers could not control the fluid loss adequately.
3. The balance between losses or gains from the producing formation appear to be very close, whole mud loss occurred both drilling and when running the casing. Although the losses were not severe on this well potential for serious problems exist and should be planned for. High mud weight to fight pressure may contribute to losses that would cause a serious well control problem.
4. Use a storage shed for mud products on location. Product bags were on location for over three (3) months and the shrink wrap started to break down. Product loss could have been a greater problem if the weather turned worse.

## WELL KICKS AND WELL CONTROL OPERATIONS: (See "Hydrocarbon Report")

Several gas shows were present in the Nahanni formation from 3657-3847m due to fractures. The density of the drilling fluid was higher than the formation mud weight equivalent, so despite high drilled gas units, gas kicks were not taken. A total of 8m<sup>3</sup> of drilling mud was lost while drilling from 3822-3834m. The losses were of a slow seepage in to the fracture system and did not create a well control problem.

There were good gas responses while drilling the Headless formation from 3847-3920m. A 1m<sup>3</sup> increase in pit volume was noted while drilling from 3883-3887m however the mud flow returned to normal in 30 minutes.

## FORMATION LEAK OFF TESTING:

A leak off test was run after drilling 10m of hole outside the casing window.

Last Casing Depth:	3273m
Mud Density:	1210 kg/m <sup>3</sup>
Surface Pressure:	20000kPa
Formation Gradient:	17.9 kPa/m

## FISHING OPERATIONS:

Lost Cones: The cones of bit #11 were left in the hole after drilling from 3630-3664.5m KB. The Nahanni formation top came in at 3657m KB and the dense dolomite of the Nahanni top likely caused the excessive wear. The cones were milled up with a flat bottom mill.

Lost Cones: The tips of the cones of bit #15 were left in the hole likely due to running excessive hours on the bit. The cone pieces were retrieved with a magnet.




# SPERRY-SUN DRILLING SERVICES

VERTICAL PROJECTION

COLUMBIA GAS DEVELOPMENT OF CANADA  
REF. IS WELLHEAD  
COLUMBIA ET AL KOTANEELEE I-48  
DD-335

START NO. = 3253  
FINISH NO. = 4415  
SCALE IS 70 METERS/CM.  
COURSE LENGTH = 0.00

PLOTTED VALUES SHOWN ARE MEASURED DEPTHS

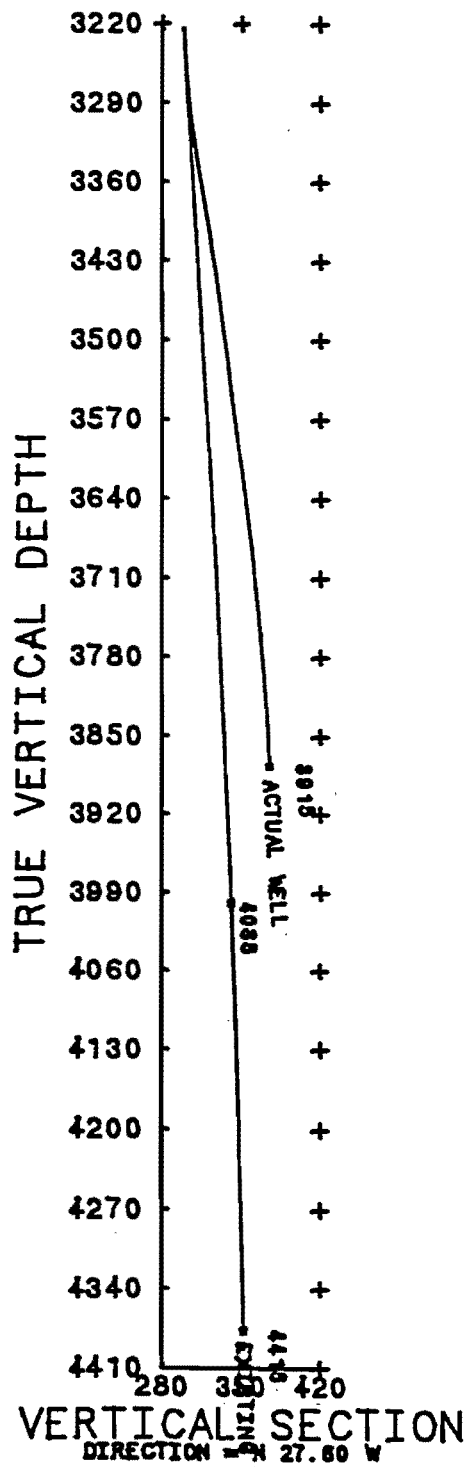



# SPERRY-SUN DRILLING SERVICES


HORIZONTAL PROJECTION



COLUMBIA GAS DEVELOPMENT OF CANADA  
REF. IS WELLHEAD  
COLUMBIA ET AL KOTANEELEE I-48  
DD-335

START MD. = 3253  
FINISH MD. = 4415  
AXIS IS TRUE NORTH  
SCALE IS 8 METERS/CM.  
COURSE LENGTH = 0.00


PLOTTED VALUES SHOWN ARE MEASURED DEPTHS

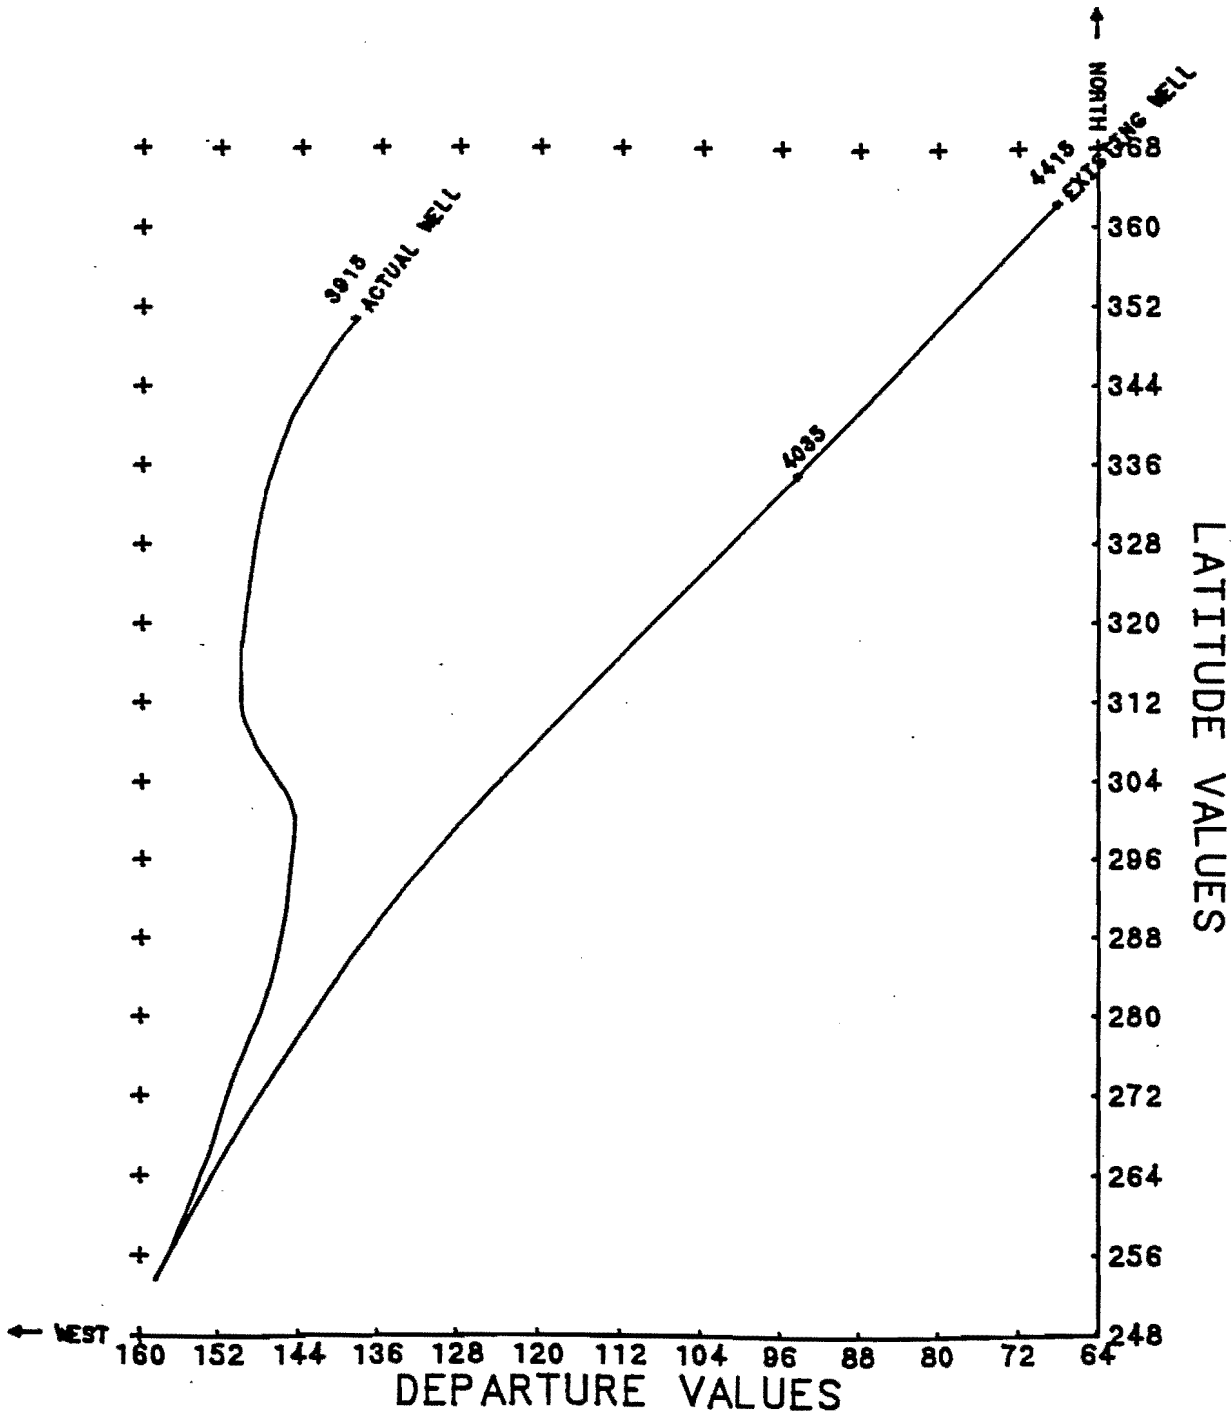

**sperry-sun**  
**DRILLING SERVICES**  
**OF CANADA**

**COMPLETION PLAN**  
**FOR**

COLUMBIA ET AL KOTANEELEE I-48



WELL: COLUMBIA ET AL KOTANEELEE I-48

L.S.D.: I-48

FIELD: KOTANEELEE

PROVINCE: NORTHWEST TERRITORIES

JOB NO.: DD-335

DATE: 1991 06 26

1991 06 26

COLUMBIA GAS DEVELOPMENT OF CANADA  
 COLUMBIA ET AL KOTANEELEE I-48  
 REFERENCE DIRECTION IS TRUE NORTH

DD-335  
 VERTICAL SECTION ALONG CLOSURE  
 DISTANCES ARE IN METERS

TOTAL MEAS DEPTH	ANGLE DEG.DEC	AZIMUTH DEG.DEC	TRUE VERTICAL DEPTH	TOTAL NORTH	CO-ORDINATES EAST	VERTICAL SECTION	DLS PER 30
0.00	0.00	0.00	0.00	0.00	0.00	0.00	
100.00	0.00	0.00	100.00	0.00	0.00	0.00	0.00
216.00	1.05	328.00	215.99	0.90	-0.56	1.05	0.27
224.00	2.08	313.00	223.99	1.06	-0.71	1.25	4.14
253.00	3.92	327.00	252.95	2.25	-1.63	2.70	2.03
282.00	4.00	325.00	281.88	3.91	-2.75	4.65	0.17
311.00	4.00	327.00	310.81	5.59	-3.88	6.62	0.14
339.00	4.00	326.00	338.74	7.22	-4.96	8.54	0.07
368.00	4.00	322.00	367.67	8.85	-6.15	10.49	0.29
396.00	3.92	324.00	395.60	10.40	-7.31	12.36	0.17
425.00	4.00	325.00	424.54	12.03	-8.48	14.30	0.11
454.00	4.00	325.00	453.46	13.68	-9.64	16.27	0.00
483.00	4.00	327.00	482.39	15.36	-10.77	18.24	0.14
511.00	4.00	324.00	510.33	16.97	-11.87	20.14	0.22
540.00	4.08	320.00	539.25	18.58	-13.13	22.10	0.30
569.00	4.42	321.00	568.17	20.24	-14.50	24.15	0.35
597.00	4.08	313.00	596.10	21.76	-15.91	26.08	0.73
626.00	4.00	311.00	625.03	23.12	-17.42	27.91	0.17
654.00	4.00	309.00	652.96	24.38	-18.92	29.62	0.15
683.00	4.08	308.00	681.88	25.65	-20.52	31.39	0.11
712.00	4.50	307.00	710.80	26.97	-22.24	33.25	0.44
740.00	4.42	304.00	738.72	28.23	-24.01	35.08	0.27
768.00	4.92	303.00	766.63	29.49	-25.91	36.95	0.54
797.00	5.00	300.00	795.52	30.80	-28.05	38.95	0.28
825.00	4.83	310.00	823.41	32.17	-30.01	40.94	0.93
854.00	5.00	309.00	852.31	33.75	-31.93	43.11	0.19
883.00	5.00	308.00	881.20	35.32	-33.91	45.30	0.09
911.00	6.00	307.00	909.07	36.95	-36.04	47.60	1.08
940.00	6.00	306.00	937.91	38.76	-38.47	50.18	0.11
969.00	6.42	306.00	966.74	40.60	-41.01	52.82	0.43
998.00	7.00	304.00	995.54	42.54	-43.79	55.65	0.65
1026.00	7.08	303.00	1023.33	44.44	-46.65	58.46	0.16
1036.00	6.92	296.00	1033.26	45.04	-47.71	59.41	2.61
1046.00	7.00	294.00	1043.18	45.55	-48.80	60.29	0.77
1050.00	7.00	295.00	1047.15	45.75	-49.25	60.64	0.91
1085.00	7.90	290.00	1081.86	47.47	-53.44	63.78	0.95
1113.00	8.50	289.00	1109.57	48.81	-57.21	66.40	0.66
1142.00	9.00	288.00	1138.23	50.20	-61.39	69.24	0.54
1170.00	9.80	286.00	1165.86	51.54	-65.76	72.08	0.93
1227.00	11.40	289.00	1221.88	54.71	-75.75	78.70	0.89

1991 06 26

COLUMBIA GAS DEVELOPMENT OF CANADA  
 COLUMBIA ET AL KOTANEELEE I-48  
 REFERENCE DIRECTION IS TRUE NORTH

DD-335  
 VERTICAL SECTION ALONG CLOSURE  
 DISTANCES ARE IN METERS

TOTAL MEAS DEPTH	ANGLE DEG.DEC	AZIMUTH DEG.DEC	TRUE VERTICAL DEPTH	TOTAL NORTH	CO-ORDINATES EAST	VERTICAL SECTION	DLS PER 30
1256.00	11.40	290.00	1250.31	56.62	-81.16	82.46	0.20
1284.00	12.00	289.00	1277.73	58.52	-86.51	86.19	0.68
1313.00	12.00	285.00	1306.10	60.28	-92.27	89.95	0.86
1341.00	11.30	290.00	1333.52	61.97	-97.66	93.50	1.32
1370.00	11.50	293.00	1361.95	64.07	-102.99	97.41	0.65
1398.00	10.80	298.00	1389.42	66.39	-107.88	101.36	1.28
1427.00	10.90	300.00	1417.90	69.04	-112.65	105.58	0.40
1455.00	11.10	301.00	1445.39	71.75	-117.26	109.79	0.30
1484.00	11.20	305.00	1473.84	74.80	-121.96	114.36	0.81
1513.00	11.30	304.00	1502.28	78.01	-126.62	119.05	0.23
1541.00	10.90	314.00	1529.76	81.38	-130.80	123.72	2.10
1570.00	11.20	303.00	1558.23	84.82	-135.13	128.51	2.20
1598.00	11.60	308.00	1585.67	88.04	-139.63	133.15	1.14
1627.00	10.90	308.00	1614.12	91.52	-144.09	138.03	0.72
1655.00	11.00	301.00	1641.61	94.52	-148.46	142.43	1.43
1684.00	10.90	303.00	1670.08	97.44	-153.14	146.86	0.41
1712.00	11.40	303.00	1697.55	100.39	-157.68	151.27	0.54
1741.00	11.70	305.00	1725.96	103.64	-162.49	156.06	0.52
1769.00	11.80	309.00	1753.38	107.07	-167.04	160.92	0.88
1798.00	11.60	310.00	1781.78	110.81	-171.58	166.07	0.29
1826.00	11.10	310.00	1809.23	114.35	-175.80	170.91	0.54
1855.00	11.90	314.00	1837.65	118.22	-180.09	176.09	1.17
1883.00	11.10	314.00	1865.08	122.10	-184.10	181.17	0.86
1912.00	11.10	310.00	1893.54	125.83	-188.25	186.16	0.80
1940.00	10.30	313.00	1921.06	129.27	-192.15	190.79	1.04
1970.00	10.10	314.00	1950.58	132.93	-196.00	195.61	0.27
1997.00	7.80	316.00	1977.25	135.89	-198.98	199.46	2.58
2026.00	7.80	320.00	2005.98	138.82	-201.61	203.14	0.56
2054.00	7.70	319.00	2033.73	141.69	-204.06	206.71	0.18
2083.00	7.20	323.00	2062.48	144.61	-206.43	210.30	0.74
2112.00	6.80	320.00	2091.27	147.37	-208.63	213.68	0.56
2140.00	6.00	328.00	2119.09	149.88	-210.47	216.69	1.28
2169.00	5.20	322.00	2147.95	152.20	-212.08	219.44	1.02
2197.00	5.10	328.00	2175.84	154.26	-213.52	221.88	0.59
2226.00	5.70	349.00	2204.71	156.77	-214.48	224.56	2.12
2254.00	5.20	5.00	2232.59	159.40	-214.63	227.07	1.71
2283.00	5.20	5.00	2261.47	162.01	-214.40	229.42	0.00
2311.00	6.30	6.00	2289.33	164.81	-214.13	231.92	1.18
2340.00	5.90	8.00	2318.16	167.86	-213.76	234.62	0.47
2368.00	5.90	7.00	2346.02	170.72	-213.38	237.14	0.11

1991 06 26

COLUMBIA GAS DEVELOPMENT OF CANADA  
 COLUMBIA ET AL KOTANEELEE I-48  
 REFERENCE DIRECTION IS TRUE NORTH

DD-335  
 VERTICAL SECTION ALONG CLOSURE  
 DISTANCES ARE IN METERS

TOTAL MEAS DEPTH	ANGLE DEG.DEC	AZIMUTH DEG.DEC	TRUE VERTICAL DEPTH	TOTAL NORTH	CO-ORDINATES EAST	VERTICAL SECTION	DLS PER 30
2397.00	5.10	2.00	2374.88	173.49	-213.16	239.63	0.96
2425.00	4.90	357.00	2402.78	175.92	-213.18	241.91	0.51
2454.00	4.90	359.00	2431.67	178.40	-213.26	244.24	0.18
2482.00	4.60	355.00	2459.57	180.71	-213.38	246.44	0.48
2511.00	4.60	12.00	2488.48	183.01	-213.24	248.52	1.41
2539.00	4.80	23.00	2516.39	185.19	-212.55	250.29	0.99
2568.00	5.10	30.00	2545.28	187.42	-211.43	251.96	0.70
2596.00	5.50	43.00	2573.16	189.48	-209.89	253.31	1.35
2625.00	6.00	47.00	2602.02	191.53	-207.84	254.46	0.66
2653.00	6.50	50.00	2629.85	193.55	-205.55	255.50	0.64
2682.00	7.00	43.00	2658.65	195.89	-203.09	256.78	1.00
2711.00	6.80	45.00	2687.44	198.40	-200.67	258.22	0.32
2739.00	6.90	46.00	2715.24	200.74	-198.29	259.52	0.17
2768.00	7.70	43.00	2744.00	203.37	-195.71	261.02	0.92
2796.00	9.20	41.00	2771.70	206.43	-192.96	262.86	1.64
2825.00	10.20	38.00	2800.28	210.21	-189.86	265.23	1.16
2853.00	9.60	40.00	2827.87	213.95	-186.83	267.60	0.74
2882.00	9.10	39.00	2856.48	217.58	-183.84	269.88	0.54
2910.00	10.10	43.00	2884.09	221.10	-180.77	272.03	1.29
2939.00	9.20	42.00	2912.68	224.68	-177.48	274.15	0.95
2967.00	8.50	43.00	2940.35	227.86	-174.57	276.04	0.77
2996.00	7.00	41.00	2969.08	230.76	-171.95	277.78	1.58
3024.00	6.50	33.00	2996.89	233.38	-169.97	279.48	1.14
3053.00	6.20	26.00	3025.71	236.16	-168.39	281.49	0.86
3081.00	5.90	34.00	3053.55	238.71	-166.92	283.33	0.96
3110.00	5.80	35.00	3082.40	241.15	-165.25	284.98	0.15
3138.00	6.00	36.00	3110.25	243.49	-163.58	286.54	0.24
3167.00	5.70	27.00	3139.10	246.00	-162.03	288.31	1.00
3195.00	5.70	35.00	3166.97	248.38	-160.60	290.00	0.85
3224.00	5.00	31.00	3195.84	250.64	-159.13	291.56	0.82
3253.00	5.20	27.00	3224.72	252.90	-157.88	293.20	0.42
3280.00	5.50	28.25	3251.61	255.13	-156.71	294.84	0.36
3325.00	11.20	19.50	3296.11	261.15	-154.23	299.54	3.88
3348.00	12.30	22.25	3318.63	265.52	-152.55	302.99	1.61
3357.00	12.80	14.25	3327.42	267.38	-151.95	304.49	6.02
3377.00	13.50	19.25	3346.89	271.73	-150.63	308.06	2.00
3397.00	14.00	24.25	3366.32	276.14	-148.87	311.51	1.93
3410.21	13.80	22.35	3379.14	279.05	-147.61	313.76	1.13
3427.00	12.40	13.25	3395.50	282.66	-146.44	316.68	4.45
3440.50	11.60	11.25	3408.70	285.40	-145.84	319.02	2.00

1991 06 26

COLUMBIA GAS DEVELOPMENT OF CANADA  
 COLUMBIA ET AL KOTANEELEE I-48  
 REFERENCE DIRECTION IS TRUE NORTH

DD-335  
 VERTICAL SECTION ALONG CLOSURE  
 DISTANCES ARE IN METERS

TOTAL MEAS DEPTH	ANGLE DEG.DEC	AZIMUTH DEG.DEC	TRUE VERTICAL DEPTH	TOTAL NORTH	CO-ORDINATES EAST	VERTICAL SECTION	DLS PER 30
452.00	11.00	12.75	3419.98	287.61	-145.37	320.89	1.74
3464.00	10.50	5.00	3431.77	289.81	-145.02	322.82	3.82
474.00	10.75	7.25	3441.60	291.64	-144.83	324.45	1.45
493.00	9.50	3.50	3460.30	294.97	-144.51	327.42	2.23
3503.00	10.25	8.25	3470.15	296.67	-144.33	328.94	3.32
520.00	7.30	358.25	3486.95	299.25	-144.15	331.27	5.84
536.00	7.50	336.75	3502.82	301.23	-144.59	333.27	5.18
3561.00	7.25	322.75	3527.62	303.98	-146.19	336.42	2.17
3580.00	7.25	325.75	3546.47	305.93	-147.59	338.75	0.60
3610.00	8.00	345.25	3576.21	309.51	-149.19	342.67	2.68
3620.00	8.50	354.25	3586.10	310.92	-149.44	344.07	4.15
3652.00	9.00	2.75	3617.73	315.77	-149.55	348.63	1.30
3664.00	9.00	5.25	3629.58	317.64	-149.42	350.32	0.98
3720.00	8.00	9.25	3684.97	325.85	-148.40	357.58	0.62
3767.00	7.75	11.25	3731.53	332.19	-147.25	363.05	0.24
3825.00	7.75	25.25	3789.00	339.56	-144.82	369.02	0.97
3882.00	8.00	34.75	3845.47	346.30	-140.92	373.85	0.70
3915.00	8.00	40.25	3878.15	349.94	-138.13	376.21	0.70


## MINIMUM CURVATURE METHOD

HORIZONTAL DISPLACEMENT AT BOTTOM HOLE IS  
 376.21 METERS ALONG 338.46 DEG  
 RELATIVE TO WELL HEAD

VERTICAL SECTION RELATIVE TO WELL HEAD

F. COMPLETION SUMMARY

# COLUMBIA ET AL KOTANEELEE YT 1-48A SIDETRACK SCHEMATIC

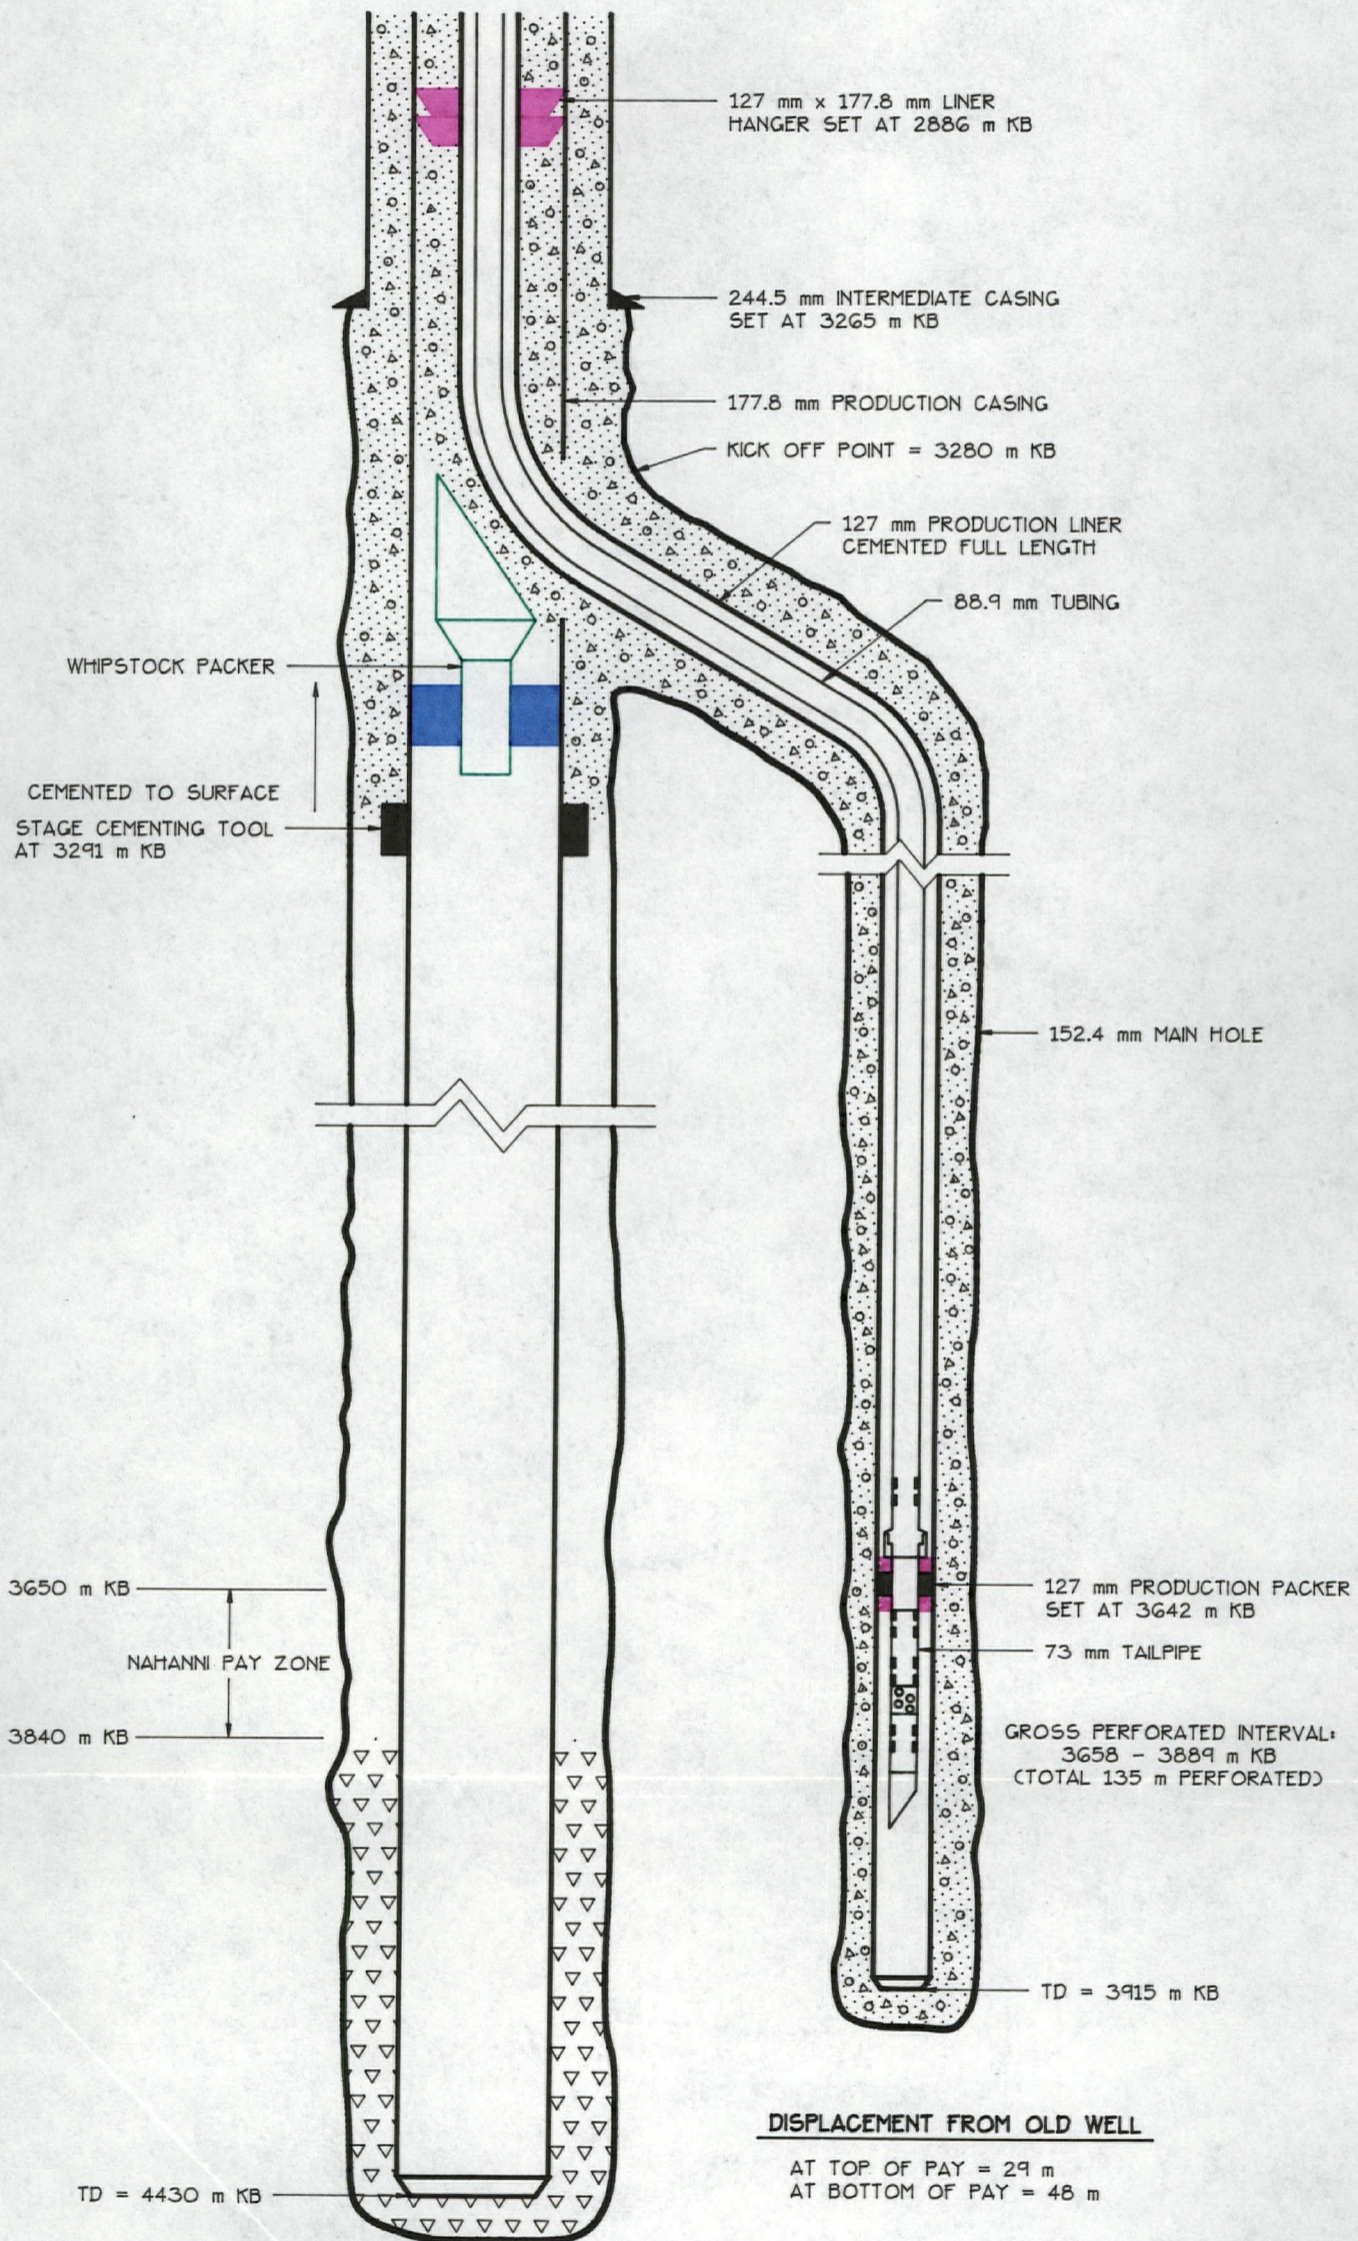



# COLUMBIA GAS DEVELOPMENT OF CANADA LTD.

STANDARD LIFE BUILDING  
 639 - 5TH AVENUE S.W.  
 CALGARY, ALBERTA, CANADA T2P 0M9  
 (403) 261-8880

## TUBING SUMMARY

Well Columbia et al Kotaneelee YT I-48A Date 91-07-07

KB Elevation 832.7m KB to CSG FLG 5.58m KB to TBG TOP 4.42m

Casing OD 177.8mm/127mm WT 47.6/26.8 kg/m MIN DIA 152.4mm/108.6mm

Set At 127mm @ 3914.5m PBD 3900m KB PERFS 3658-3889m KB

Tubing OD 89mm WT 13.84 kg/m Type L-80, CSH Make Hydril

No. Joints on Location 399 Tally 3788.65m

No. Joints Run 382 Tally 3630.02m

### PERMANENT STRING FROM BOTTOM UP


No. Joints	Description	Measured Length	KB Depth	Remarks
73mm	Wireline re-entry guide	0.15	3652.72	
73mm	CS Hydril pup joint	0.61		
73mm	Otis "XN" nipple	0.33	3651.63	58.7mm profile
73mm	CS Hydril pup joint	2.98		
73mm	Perforated pup	2.99		
73mm	Otis "X" nipple	0.32	3645.34	58.7mm profile
73mm	CS Hydril pup joint	1.78		
73mm	Otis "X" nipple	0.22	3643.34	58.7mm profile
Packer	20-144-510 Model SO	1.10	3642.24	
89mm	On-Off tool, 1/4 turn	0.52		
	right hand release			

Total String Length \_\_\_\_\_

KB to Tubing Top \_\_\_\_\_

String Depth KB \_\_\_\_\_

Remarks Continued on page 2



# COLUMBIA GAS DEVELOPMENT OF CANADA LTD.

STANDARD LIFE BUILDING  
639 - 5TH AVENUE S.W.  
CALGARY, ALBERTA, CANADA T2P 0M9  
(403) 261-8680

## TUBING SUMMARY

Page 2

Well Columbia et al Kotaneelee YT I-48A Date 91-07-07

KB Elevation \_\_\_\_\_ KB to CSG FLG \_\_\_\_\_ KB to TBG TOP \_\_\_\_\_

Casing OD \_\_\_\_\_ WT \_\_\_\_\_ MIN DIA \_\_\_\_\_

Set At \_\_\_\_\_ PBD \_\_\_\_\_ PERFS \_\_\_\_\_

Tubing OD \_\_\_\_\_ WT \_\_\_\_\_ Type \_\_\_\_\_ Make \_\_\_\_\_

No. Joints on Location \_\_\_\_\_ Tally \_\_\_\_\_

No. Joints Run \_\_\_\_\_ Tally \_\_\_\_\_

### PERMANENT STRING FROM BOTTOM UP

No. Joints	Description	Measured Length	KB Depth	Remarks
89mm	CS Hydril pup	2.37		
89mm	Otis "X" nipple	0.31	3639.04	58.7mm profile
381	jts. 89mm CSH tubing	3620.65		
1	89mm pup	1.16		
1	89mm pup	1.70		
1	89mm pup	2.38		
1	89mm pup (double pin)	0.16		
1	jt. 89mm hydril tubing	9.37		
	squat on packer	-0.80		

Total String Length	3648.30
KB to Tubing Top	4.42
String Depth KB	3652.72

Remarks 7000 daN compression set on packer.

-177.8mm x 127mm casing and packer tested to 31 MPa for 15 mins.

- 89mm tubing, packer & 127mm casing tested to 35 MPa for 15 mins.


Field Supervisor \_\_\_\_\_

PERFORATION RECORD

COLUMBIA ET AL KOTANEELEE Y.T. I-48A

INTERVAL (m KB)	LENGTH (m)
3889.0-3859.0	30.0
3859.0-3844.0	15.0
3844.0-3837.5	6.5
3829.0-3814.0	15.0
3789.0-3774.0	15.0
3769.0-3758.5	10.5
3746.0-3739.0	7.0
3724.0-3709.0	15.0
3693.0-3687.0	6.0
3678.0-3668.0	10.0
3663.0-3658.0	5.0
	<hr/>
	<u>135.0</u>

All perforations shot with a 54mm, DS gun loaded with 25A Ultrajet HMX high temperature charges at 13 jspm and 60 degree phasing.



An International Company

WELL SERVICE LTD.

1300, 801 - 6th AVENUE S.W., CALGARY, ALBERTA, CANADA T2P 4E1 TELEPHONE (403) 261-2990 TELEX 03-825617 FACSIMILE (403) 264-7242

ACID TREATMENT TREATMENT REPORT

T.R. Number : 012775 Rev : 01  
Customer Name: COLUMBIA GAS DEVELOPMENT OF CANADA  
1000 STANDARD LIFE BLDG.  
639 - 5TH AVENUE S.W.  
CALGARY AB  
T2P 0M9  
Contractor : KENTING 7  
Customer Rep.: HAROLD RUGG

Customer Job #: 17368  
Service order#: C5340 ✓  
Province : YT  
Well Location :  
Well Name : COLUMBIA ET AL KOTANEELEE  
Job Type : ACID TREATMENT  
Nowsco Rep. : MILLER HENDREN

I-48A

Well Data

	Size (mm)	Top (m)	Bottom (m)	Density (kg/m)	Volume (m3)	Allowable Pressure (MPa)
THIRING	89.0	0.00	3642.00	13.84	16.80	35.00
ING	73.0	3642.00	3653.00	9.67		
ASING	127.0	0.00	3914.50	26.79	2.19	12.00

Total Volume : 18.99 m3

Perfs From 3658.0 m To 3889.0 m Density 13 shots/n

Arrived At Location: 91/07/17 08:00:00 Left Location : 91/07/17 15:30:00

Pressure

Instantaneous Shut In : 3.50 MPa Pressure Test : 41.50 MPa

Fluid Details

Fluid Description	Additive List
56.50 m3 15% HCl acid	With 15% HCl acid At 15.000 m3/m3 blended

continued...


ACID TREATMENT TREATMENT REPORT

R. Number : 012775 Rev : 01  
 Customer Name: COLUMBIA GAS DEVELOPMENT OF CANADA  
 Location :  
 Well Name : COLUMBIA ET AL KOTANEELEE

Service order#: C5340  
 Customer Job #: 17368  
 Job Type : ACID TREATMENT

----- Job Details -----

Remarks	Product	Time	Pressure(MPa)				<----- Gas or Fluid m3 ----->	
			Casing	Tubing	out of tanks	per Reading	in Form.	per minute
Rig in		0920.0						
Safety Meeting		0929.0						
Pressure up		0936.0	11.80					
Pressure test to 41.500 MPa		1004.0	7.00	41.50				
Start	15% HCl acid	1009.0	10.40	30.00				
Stop Pump		1043.0	2.00	4.00	20.00	20.000	1.01	0.60
Start		1056.0	2.00					
Stop Pump		1058.0	2.10	4.00	22.00	2.000	3.01	0.70
Start		1109.0		0.80				
Start		1130.0	4.50	4.00	42.00	20.000	23.01	0.95
Stop Pump		1144.0	8.60	4.90	56.50	14.500	37.51	1.00
Start		1148.0	8.50	1.00				
Stop Pump		1155.0	9.00	6.80	64.50	8.000	45.51	1.10
Start		1216.0	11.00	2.00				
Stop Pump		1223.0	9.00	10.50	72.50	8.000	53.51	1.30
Start		1236.0	9.50	3.00				
Stop Pump		1238.0	9.70	10.80	75.50	3.000	56.50	1.30

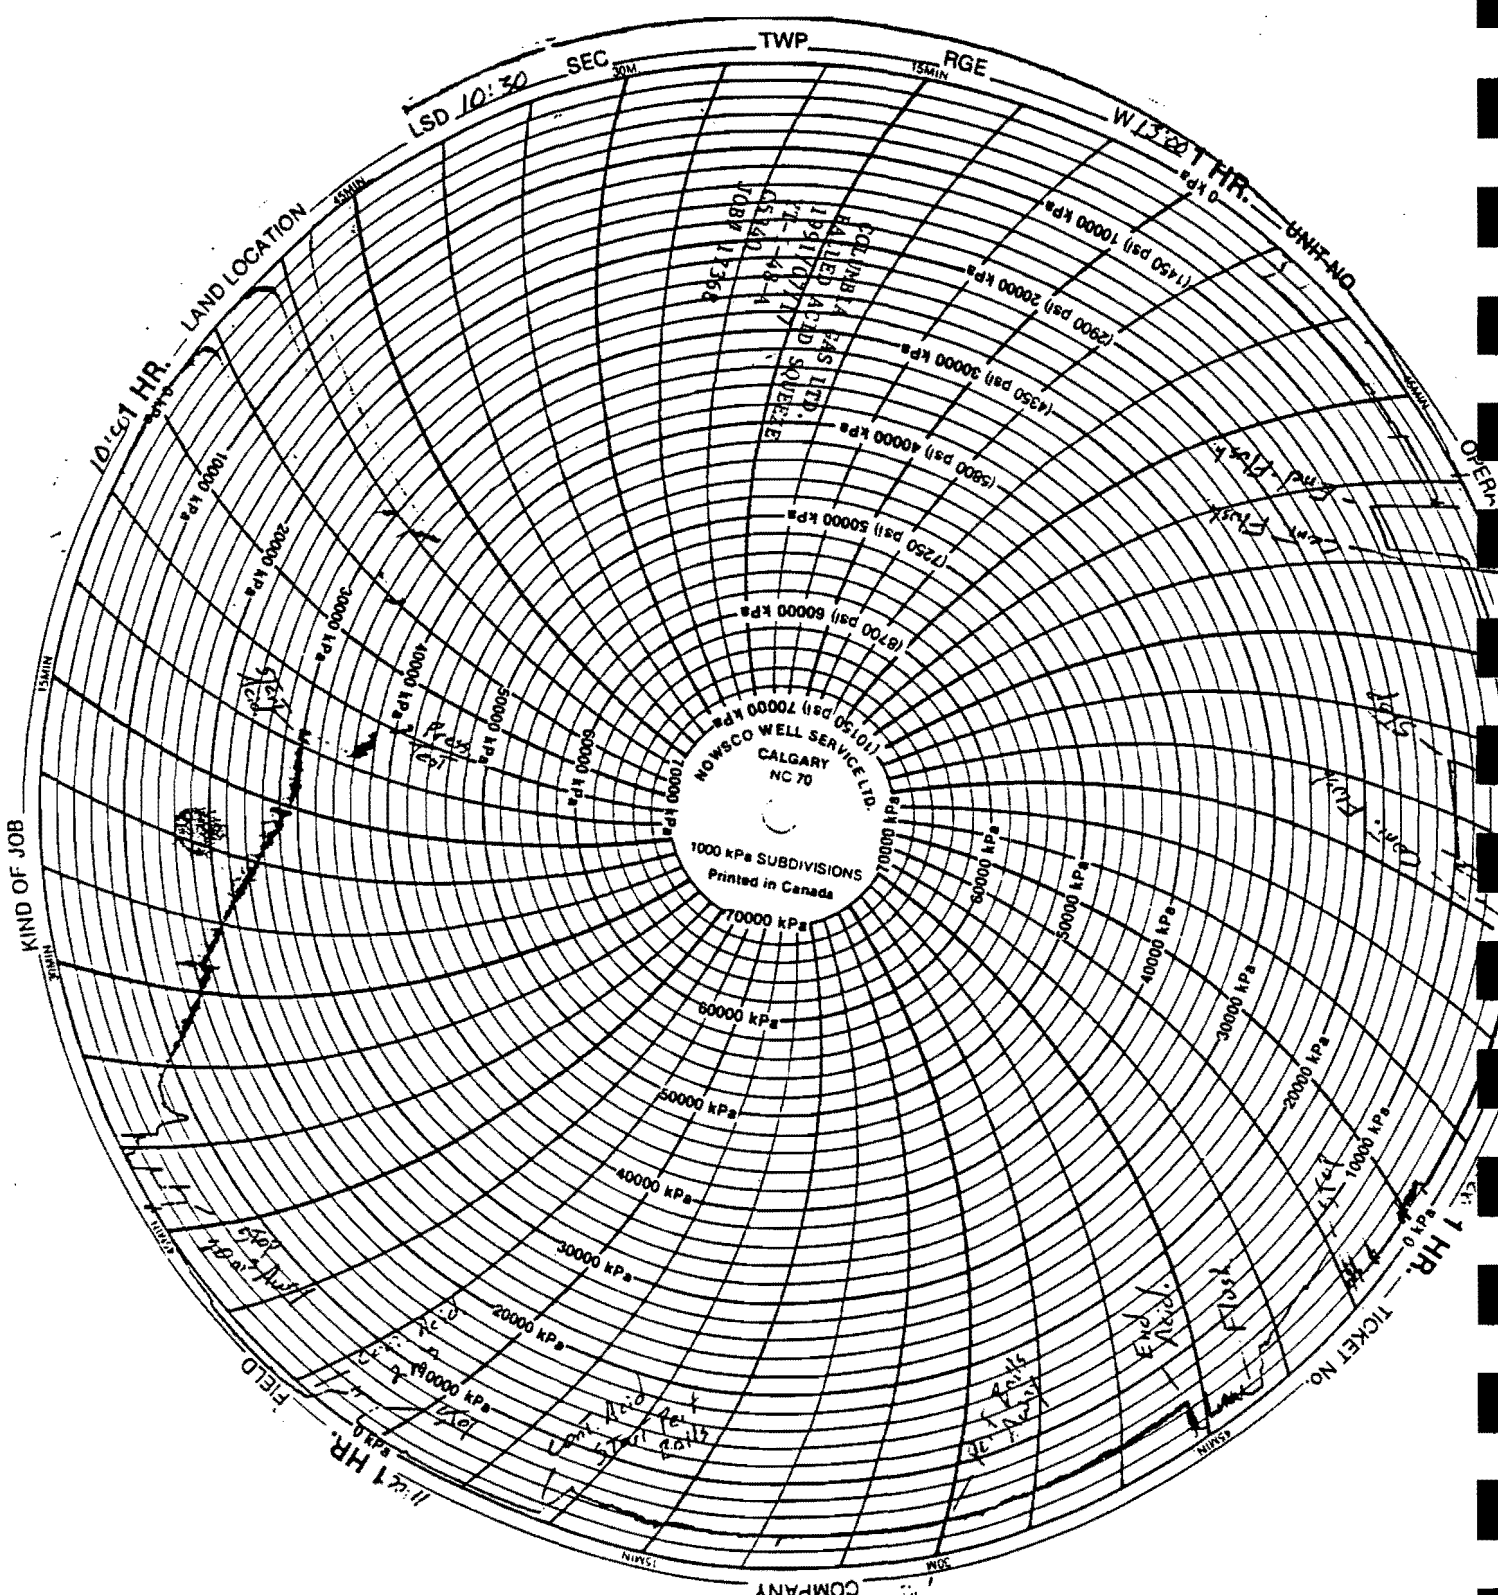

COLUMBIA GAS LTD.  
195170777 SQUEEZE  
JOB 17358

WESCO WELL SERVICE LTD.  
CALGARY NC 70  
1000 kPa SUBDIVISIONS  
Printed in Canada

KIND OF JOB

LAND LOCATION

10:30

SEC TWP RGE

W1320 TWP.

UNF-AO

1 HR.

TICKET NO.

COMPANY

FIELD

10:30

1 HR.

Exp. Field

10:30



**NORTHLAND  
PRODUCTION TESTING LTD.**

**PRODUCTION SUMMARY**

Customer: COLUMBIA GAS DEVELOPMENT OF CANADA LTD.  
 Test: CLEAN UP  
 Duration: 91/07/12 0330 hrs. to 91/07/21 1000 hrs.

Well: COLUMBIA et al KOTANEELEE  
 L.S.D. # Y-T-I-48 A  
 Formation: NAHANNI

DATE	TIME	FLOW TIME	WELLHEAD			Choke or Orif.	H2S %	GAS		CONDENSATE OR OIL				WATER			
			Tbg. Press	Flow Temp	Csg. Press			Q 10 <sup>3</sup> m <sup>3</sup>	Cumm. Prod. 10 <sup>3</sup> m <sup>3</sup>	Avg. hourly m <sup>3</sup> /hr	Cumm. Prod. m <sup>3</sup>	Sp.Gr 60°F	Grind Out	Avg. hourly m <sup>3</sup> /hr	Cumm. Prod. m <sup>3</sup>	Salin. ppm	PH
91/07/12	0600	2.5	7470	24		25.4	1.9	497.78	51.9988					2.71	20.76	104219	6.0
91/07/12	1400	10.5	7950	43		25.4		543.97	225.643					1.88	38.50	90625	5.0
91/07/12	2200	18.5	8690	52		25.4		569.78	411.249					1.25	50.71	81563	5.0
91/07/13	0600	26.5	8940	56		25.4	2.0	589.96	605.241					1.36	61.67	63438	5.0
91/07/13	1400	34.5	9120	60		25.4		609.87	805.852					1.25	73.14	58906	5.0
91/07/13	2200	42.5	9440	63		25.4		619.19	1010.64					1.25	83.58	63438	5.0
91/07/14	0600	50.5	9540	64		25.4	1.9	626.39	1218.55					1.25	93.49	58906	5.0
91/07/14	1400	58.5	9690	66		25.4		639.85	1429.85					1.25	103.93	63438	5.0
91/07/14	2200	66.5	10000	67		25.4		644.93	1644.29					1.15	113.84	58906	7.0
91/07/15	2200	4.0	9660	54		25.4		646.72	1927.35					1.25	127.19	58906	7.0
91/07/16	0600	12.0	9740	64		25.4	1.9	642.53	2141.81					1.15	137.21	58906	6.0
91/07/16	1400	20.0	9820	67		25.4		647.21	2356.97					1.25	147.44	54375	6.0
91/07/16	2200	0.8	12070	58		25.4		701.01	2513.91					0.97	154.01		
91/07/17	0600	8.8	11140	67		25.4	1.9	640.47	2729.69					1.04	163.30	58906	6.0
91/07/17	2200	5.3	20580	81		19.45		974.17	274.402					2.92	45.91	145000	4.0
91/07/18	0600	13.3	20910	89		19.45	1.7	987.31	601.123					1.88	63.65	108750	4.0
91/07/18	1400	21.3	20930	91		19.45		968.73	928.669					1.77	79.09	95156	5.0
91/07/18	2200	29.3	20800	91		19.45		986.31	1257.69					1.57	92.87	77031	4.0
91/07/19	0600	37.3	20660	92		19.45	1.9	990.24	1587.00					1.57	105.80	72500	4.0
91/07/19	1400	45.3	30110	73		7.94		309.99	1747.10					0.31	111.33	13590	3.0
91/07/19	2200	53.3	30030	65		7.94		312.61	1851.27					0.21	114.88	13590	3.0
91/07/20	0600	61.3	30000	61		7.94	1.9	317.84	1956.65					0.31	117.28	13590	3.0
91/07/20	1400	69.3	29970	60		7.94		322.43	2063.42					0.31	119.79	13590	3.0
91/07/20	2200	77.3	29950	60		7.94		325.32	2171.54					0.31	121.98	13590	3.0
91/07/21	0600	85.3	29940	59		7.94	1.9	327.79	2280.32					0.21	124.59	13590	3.0
91/07/21	0800	87.3	29930	59		7.94		328.40	2307.66					0.73	125.63		

DATE TIME DESCRIPTION

DATE	TIME	DESCRIPTION
Y-T-I-48 A	91/07/12	02:30 LAST RUN FOR PERFORATING COMPLETE
		02:40 RIG OUT SCHLUMBERGER
		03:30 OPEN WELL ON 12.70 mm CHOKE
		03:30 SP. GR. OF 0.711 USED FOR FLOW RATE CALCULATIONS
		03:30 pPc = 4996.0 kPa pTc = 206.3 DEG. K.
		03:30 LIQUID TO SURFACE
		03:30 CASINGS OPEN TO ATMOSPHERE
		03:35 INCREASE CHOKE TO 17.46 mm / GAS TO SURFACE
		03:37 METER IN SERVICE 66.68 mm ORIFICE PLATE
		03:50 INCREASE CHOKE TO 25.40 mm
		03:57 DECREASE BACK PRESSURE
		17:05 INCREASE BACK PRESSURE
		18:00 CO2 = 11% (GASTECH)
	91/07/13	06:00
18:00		CO2 = 14%
18:30		INCREASE BACK PRESSURE
91/07/14	06:00	CO2 = 14% (GASTECH)
	18:00	CO2 = 14% (GASTECH)
	19:01	INCREASE BACK PRESSURE
91/07/15	03:00	CO2 = 14% (GASTECH)
	03:30	METER OUT OF SERVICE / SHUT IN WELL FOR BUILDUPS

	DATE	TIME	DESCRIPTION
Y-T-I-48 A	91/07/15	07:00	RIG UP SCHLUMBERGER TO DO SPINNER SURVEY
		08:25	OPEN WELL ON VARIOUS CHOKE SETTINGS FOR SPINNER
		08:25	SURVEY
		08:25	METER IN SERVICE 66.68 mm ORIFICE PLATE
		10:25	INCREASE CHOKE AS DIRECTED BY SCHLUMBERGER
		10:35	LIQUID TO SURFACE
		10:55	SHUT IN WELL / TOOLS MALFUNCTIONED
		11:25	PRESSURE UP TO CHOKE
		11:26	OPEN WELL ON 10.72 mm CHOKE
		11:26	METER IN SERVICE 66.68 mm ORIFICE PLATE
		11:35	SHUT IN WELL / TOOLS MALFUNCTIONED
		15:45	OPEN WELL ON 10.72 mm CHOKE
		15:45	METER IN SERVICE 66.68 mm ORIFICE PLATE
		16:04	INCREASE CHOKE TO 12.70 mm
		16:10	SHUT IN WELL / END OF SURVEY / SCHLUMBERGER RUN
		16:10	OUT OF HOLE
		17:30	RIG OUT SCHLUMBERGER
		17:59	PRESSURE UP TO CHOKE
		18:00	OPEN WELL ON 25.40 mm CHOKE
		18:05	LIQUID TO SURFACE
		18:10	METER IN SERVICE 66.68 mm ORIFICE PLATE

DATE TIME DESCRIPTION

DATE	TIME	DESCRIPTION	
Y-T-I-48 A	91/07/16	06:00 CO2 = 14% (GASTECH)	
		19:00 SHUT IN WELL / RIG UP NOWSCO AND PERF BALL CATCHER	
		20:15 PRESSURE UP TO CHOKE	
		20:17 DEPRESSURE FLOWLINE TO FIX LEAK AT BALL CATCHER	
		21:15 OPEN WELL ON 25.40 mm CHOKE	
		21:20 METER IN SERVICE 66.68 mm ORIFICE PLATE	
		21:25 LIQUID TO SURFACE	
		21:40 ADJUST BACK PRESSURE	
	91/07/17	06:00	CO2 = 14% (GASTECH)
		08:40	SHUT IN WELL / RIG UP NOWSCO FOR ACID JOB
08:40		PRESSURE TEST TO 31 mPA	
08:45		NEW LIQUID AND GAS CUMMULATIVE	
13:34		PRESSURE UP TO CHOKE	
13:35		OPEN WELL ON VARIOUS CHOKE SETTINGS / BOTH CASINGS	
13:35		OPEN TO ATMOSPHERE	
14:05		INCREASE CHOKE TO 17.46 mm	
14:11		INCREASE CHOKE TO 19.84 mm	
14:15		SHUT IN WELL / INSPECT BALL CATCHER	
14:24		PRESSURE UP TO CHOKE	
14:25		OPEN WELL ON 19.84 mm CHOKE	
14:45		METER IN SERVICE 66.68 mm ORIFICE PLATE	


DATE TIME DESCRIPTION

DATE	TIME	DESCRIPTION
Y-T-I-48 A	91/07/17	15:17 INCREASE BACK PRESSURE
		16:00 SHUT IN WELL / RIG OUT PERF BALL CATCHER
		16:00 247 PERF BALLS RECOVERED
		16:44 PRESSURE UP TO CHOKE
		16:45 OPEN WELL ON 15.88 mm CHOKE
		16:50 METER IN SERVICE 69.85 mm ORIFICE PLATE
		16:55 INCREASE CHOKE TO 18.26 mm
		16:58 INCREASE CHOKE TO 19.45 mm
		17:05 INCREASE CHOKE TO 21.03 mm
		17:31 INCREASE CHOKE TO 21.83 mm
		20:01 DECREASE CHOKE TO 21.03 mm
		21:01 DECREASE CHOKE TO 19.45 mm
	91/07/18	06:00
14:10		LOSS OF SUPPLY GAS
15:05		INCREASE BACK PRESSURE
91/07/19	06:00	CO2 = 14%
	08:10	DECREASE CHOKE TO 7.94 mm AS DIRECTED
	09:03	METER OUT OF SERVICE
	09:10	METER IN SERVICE 50.80 mm ORIFICE PLATE
	09:11	INCREASE BACK PRESSURE
	09:25	METER OUT OF SERVICE


DATE TIME DESCRIPTION

DATE	TIME	DESCRIPTION
Y-T-I-48 A	91/07/19	09:35 ADJUST BACK PRESSURE
	09:50	METER IN SERVICE 50.80 mm ORIFICE PLATE
	11:03	DECREASE CHOKE TO 7.54 mm
	11:08	METER OUT OF SERVICE
	11:28	METER IN SERVICE 47.63 mm ORIFICE PLATE
	11:40	METER OUT OF SERVICE / ADJUST BACK PRESSURE
	11:50	INCREASE BACK PRESSURE
	11:50	METER IN SERVICE 47.63 mm ORIFICE PLATE
91/07/20	06:00	CO2 = 14%
91/07/21	04:00	C&G LABS HP GAS SAMPLES # 9423 # 3210
	06:00	CO2 = 14%
	08:00	SHUT IN WELL FOR BUILDUPS
	10:00	END OF TEST / RIG OUT EQUIPMENT


*Tubing and Separator Pressure  
Clean Up Y-T-I-48 A  
Columbia et al Kotaneelee / Nahanni*

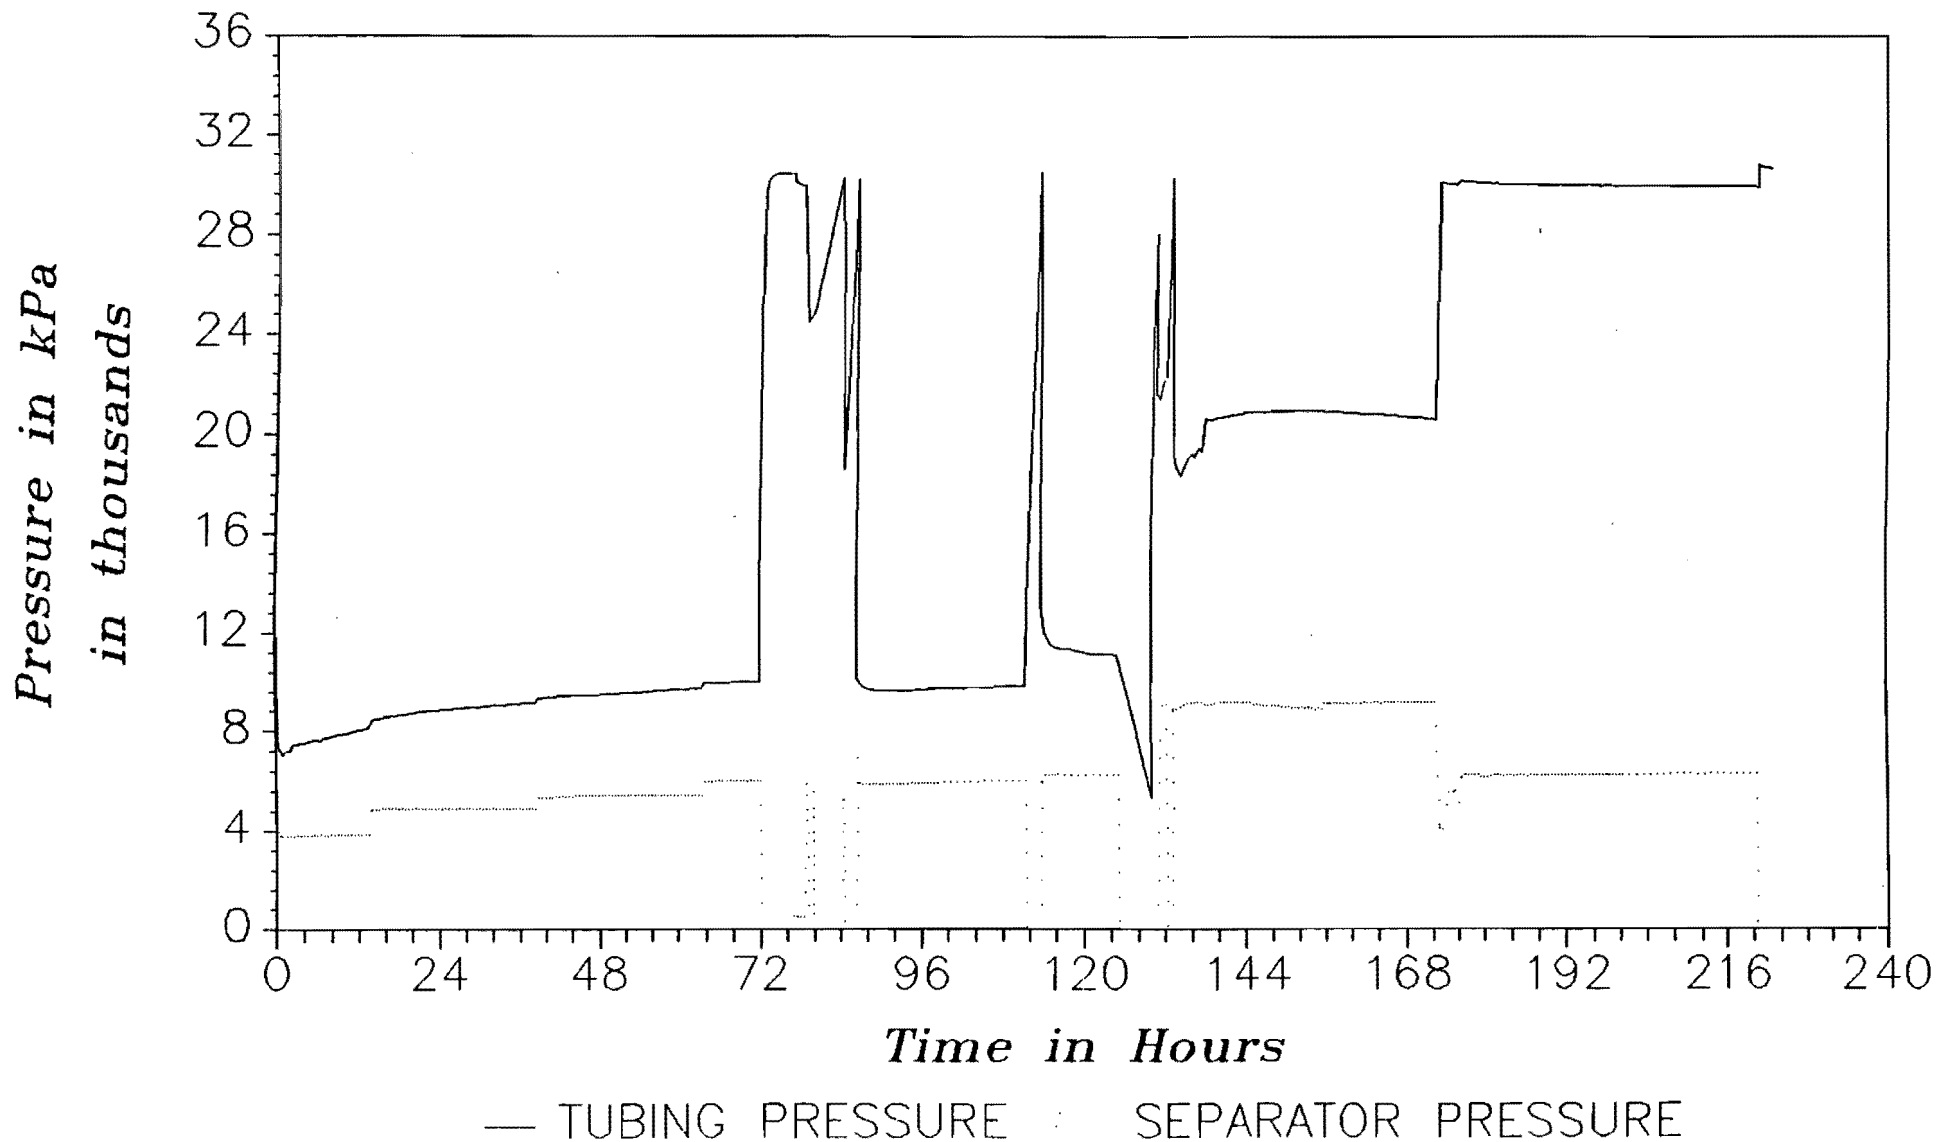


*Flow Rate  
Clean Up Y-T-I-48 A  
Columbia et al Kotaneelee / Nahanni*

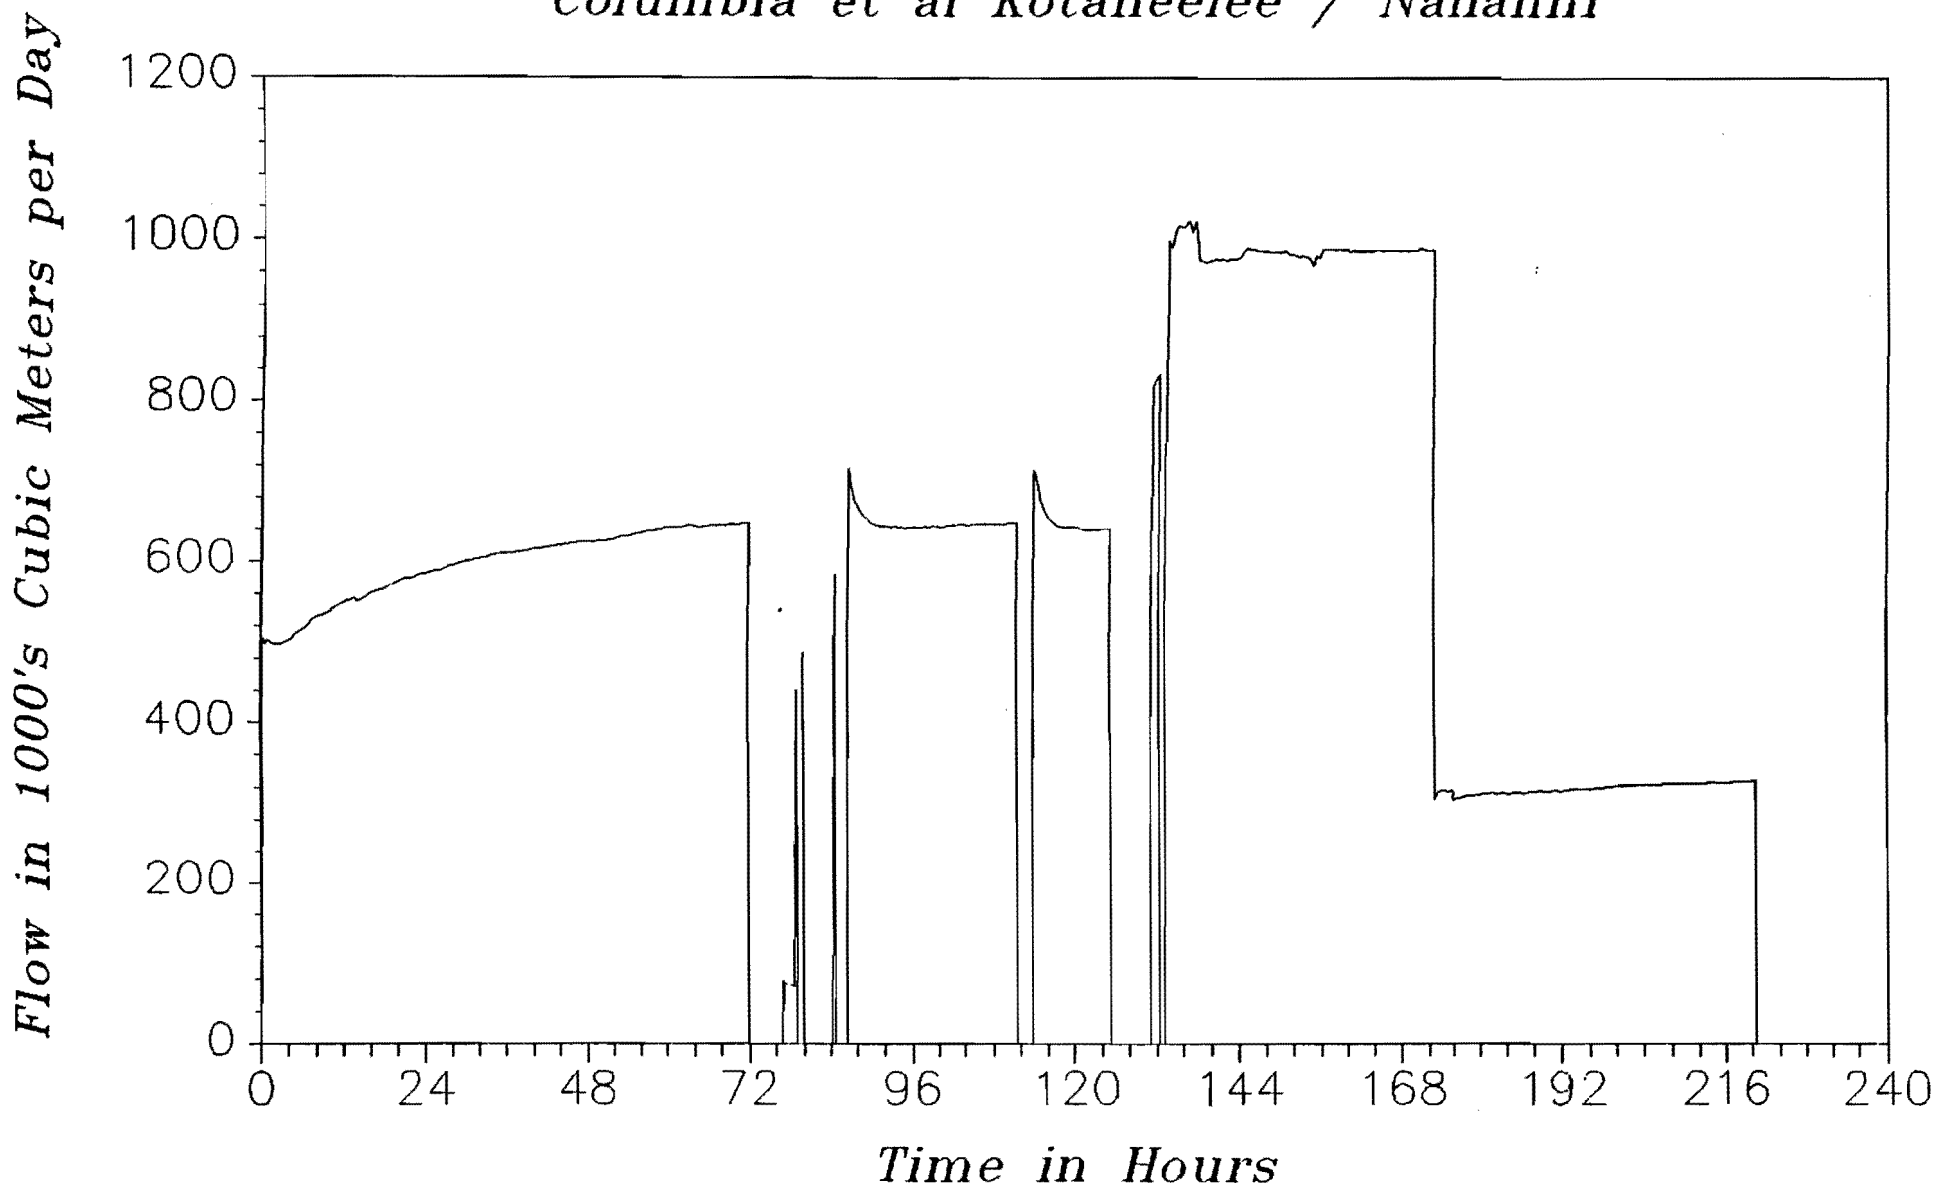


*Wellhead and Separator Temperature  
Clean Up Y-T-I-48 A  
Columbia et al Kotaneelee / Nahanni*

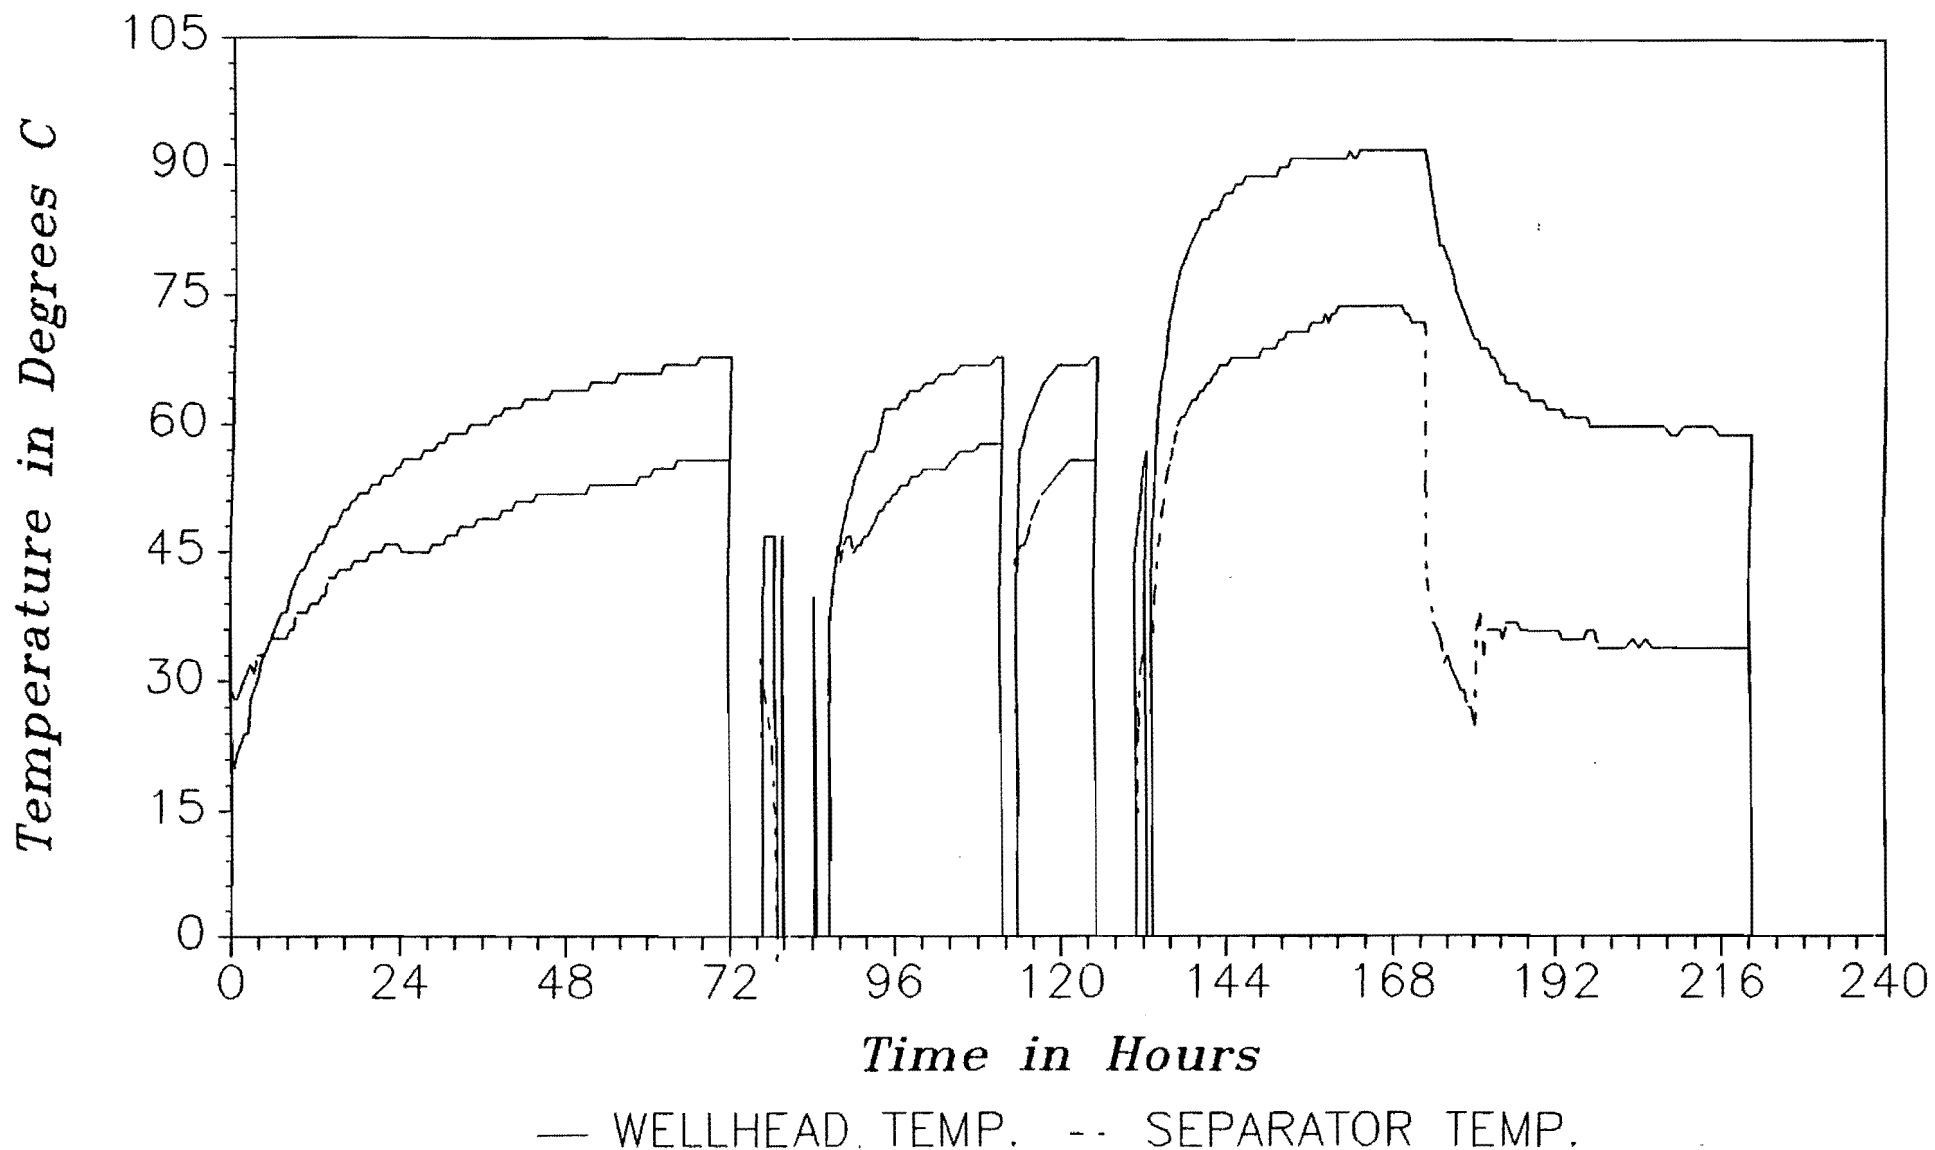

*Hourly Water Rate  
Clean Up Y-T-I-48 A  
Columbia et al Kotaneelee / Nahanni*

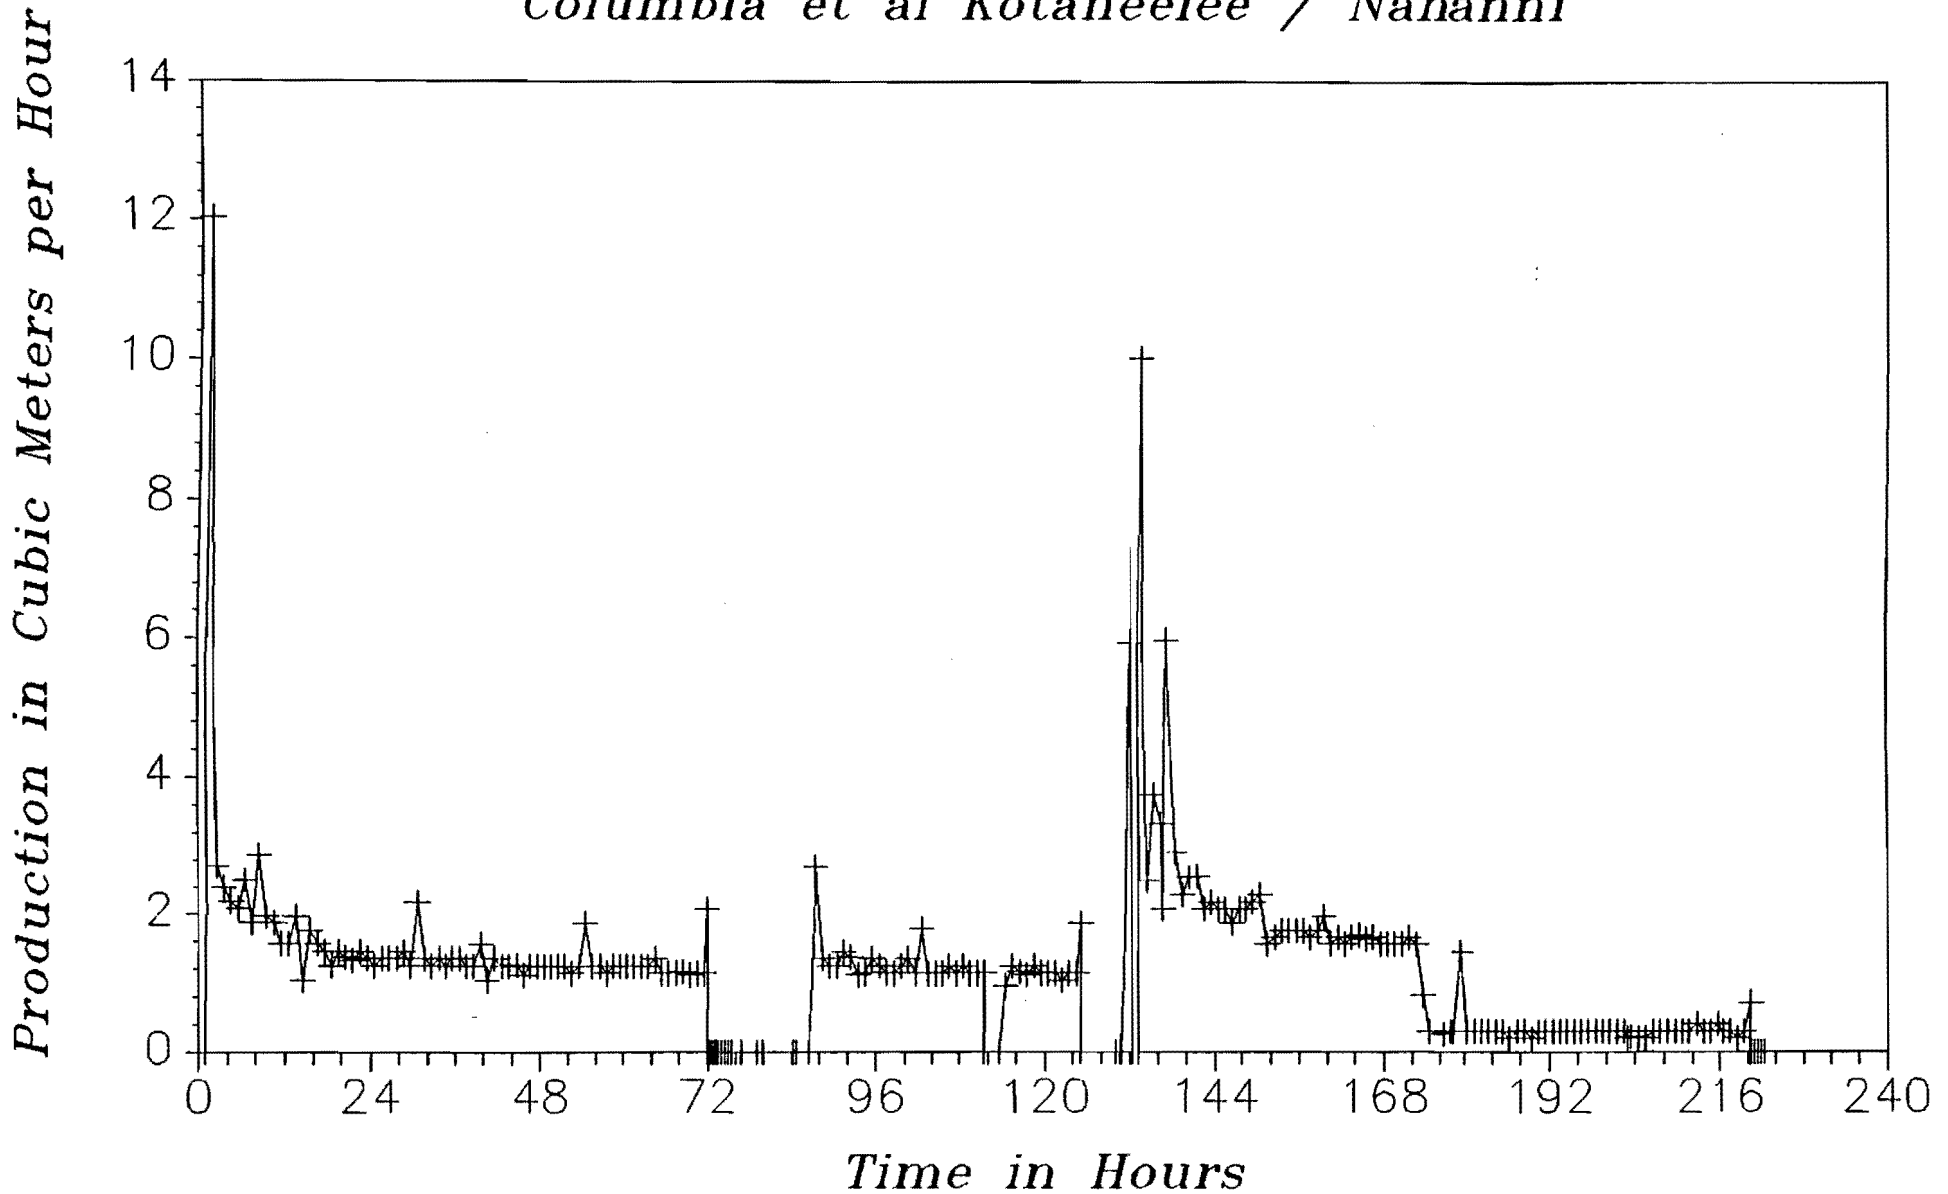

*Water / Gas Ratio  
Clean Up Y-T-I-48 A  
Columbia et al Kotaneelee / Nahanni*

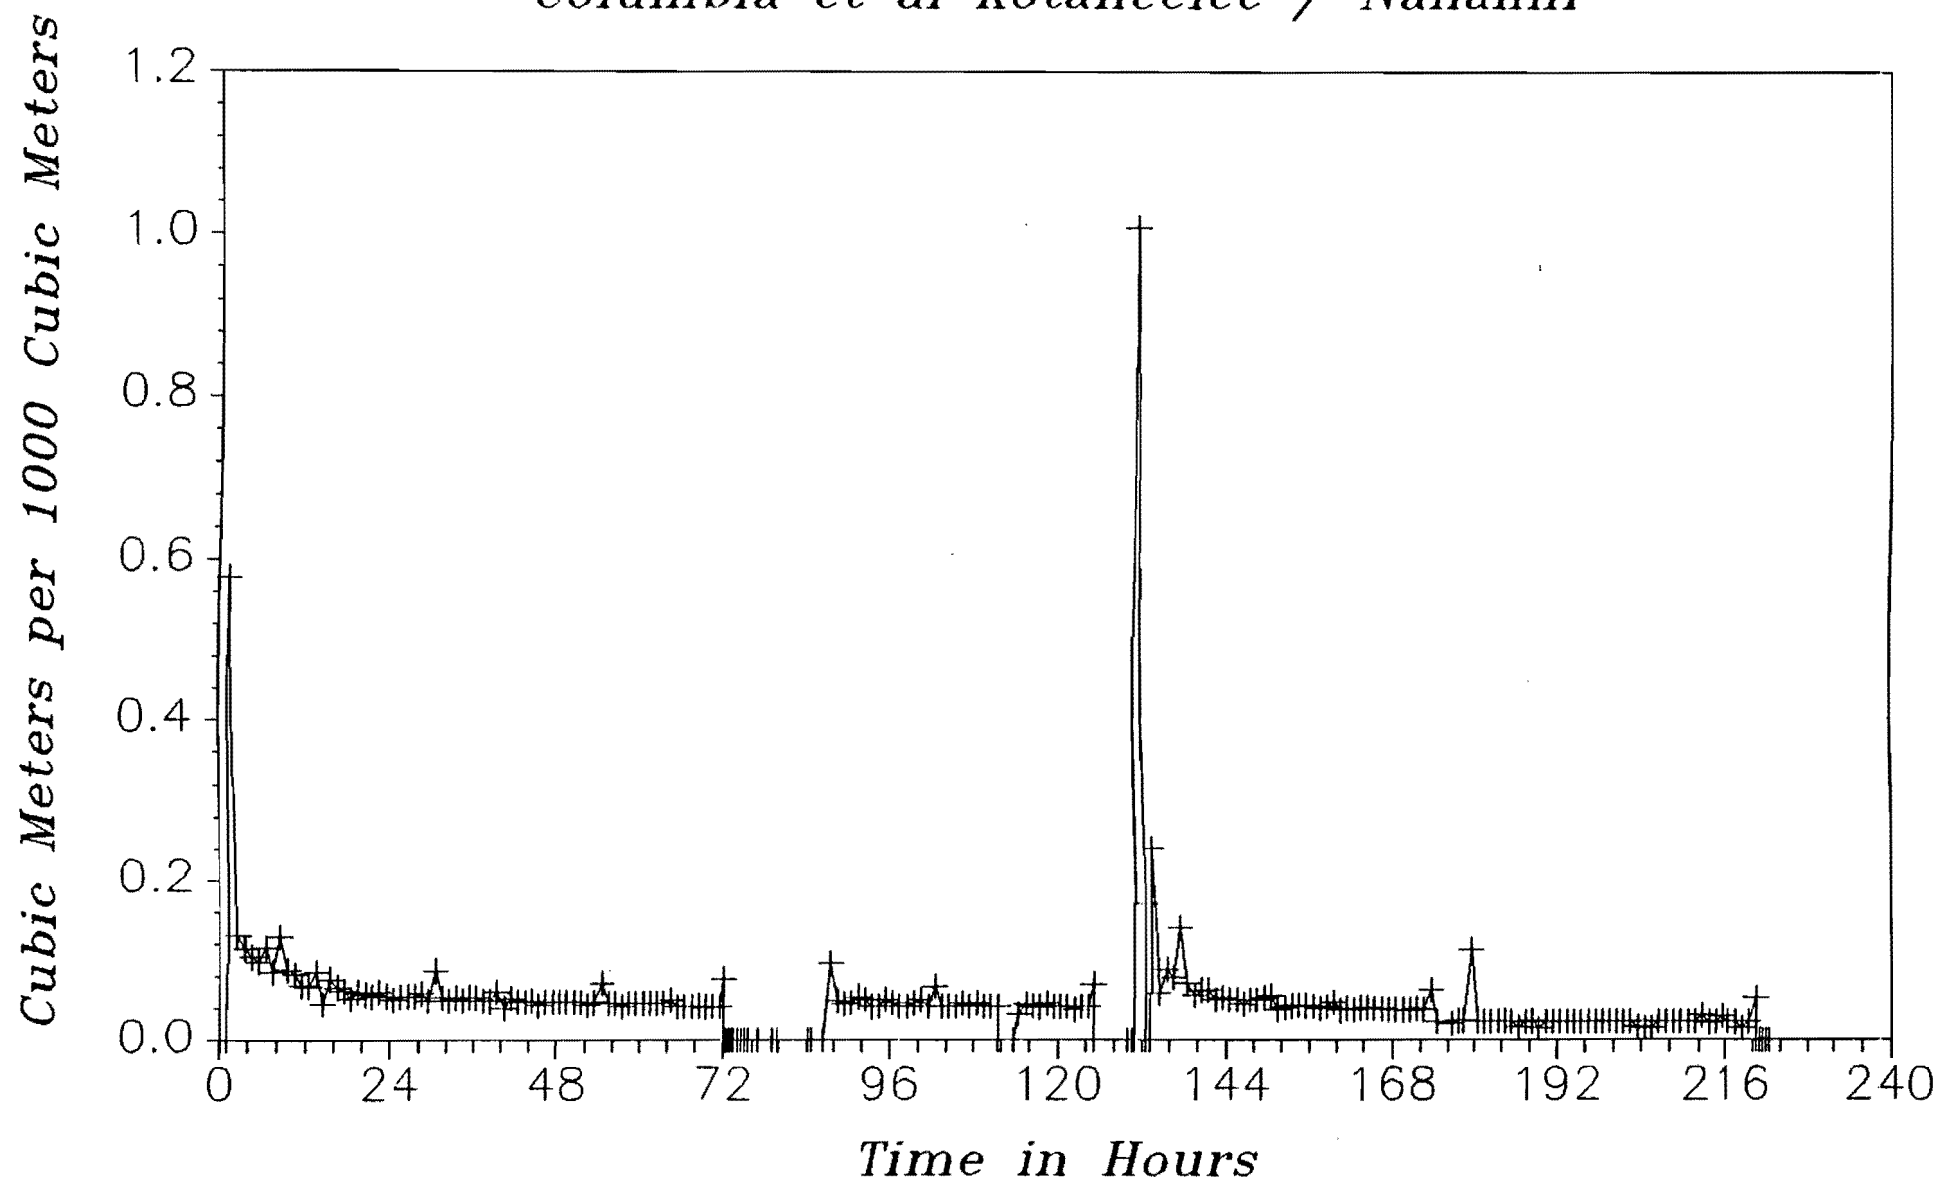



GAS ANALYSIS

CONTAINER IDENTITY: 3210, 9423      LABORATORY NUMBER: 091-1333

LICENCE NUMBER:      OPERATOR NAME: COLUMBIA GAS DEVELOPMENT OF CANADA LTD.

LOCATION: \* SEE BELOW      WELL NAME: COLUMBIA ET AL KOTANEELEE YT I-48ST

FIELD OR AREA:      POOL OR ZONE: NAHANNI      NAME OF SAMPLER:      COMPANY: NORTHLAND

TEST TYPE:      NO.:      TEST RECOVERY: \* 60-07-35.90-124 07 36.50

MULTIPLE RECOVERY: Y N

SAMPLING POINT: METER RUN      AMT & TYPE OF CUSHION:      MUD RESISTIVITY: " 25°C

TEST INTERVAL (metres):      TYPE OF PRODUCTION: PUMPING FLOWING GAS LIFT SWAB

PERFORATIONS (metres): 3658 - 3889      PRODUCTION RATES: WATER m<sup>3</sup>/d OIL m<sup>3</sup>/d GAS 10<sup>3</sup>m<sup>3</sup>/d

GAUGE PRESSURE kPa: SEPARATOR 6260 TREATER RESERVOIR SOURCE SAMPLED 6260 RECEIVED 6400

TEMPERATURE °C: SEPARATOR 34 TREATER RESERVOIR SOURCE SAMPLED RECEIVED 23

DATE SAMPLED (Y-M-D): 91-07-21      DATE RECEIVED (Y-M-D): 91-07-26      DATE REPORTED (Y-M-D): 91-07-29      ANALYST: B. ANDERSON      OTHER INFORMATION:

COMP	MOLE FRACTION		PETROLEUM LIQUID CONTENT ml/m <sup>3</sup>
	AIR FREE AS RECEIVED	AIR FREE ACID GAS FREE	
H <sub>2</sub>	0.0001	0.0001	
He	0.0008	0.0009	
N <sub>2</sub>	0.0394	0.0464	
CO <sub>2</sub>	0.1352	0.0000	
H <sub>2</sub> S	0.0165	0.0000	
C <sub>1</sub>	0.8077	0.9522	
C <sub>2</sub>	0.0003	0.0004	
C <sub>3</sub>	0.0000	0.0000	0.0
IC <sub>4</sub>	0.0000	0.0000	0.0
NC <sub>4</sub>	0.0000	0.0000	0.0
IC <sub>5</sub>	0.0000	0.0000	0.0
NC <sub>5</sub>	0.0000	0.0000	0.0
C <sub>6</sub>	0.0000	0.0000	0.0
C <sub>7</sub> +	0.0000	0.0000	0.0
C <sub>8</sub>			
C <sub>9</sub>			
C <sub>10</sub> +			

GROSS HEATING VALUE MJ/m<sup>3</sup> 15°C AND 101.325 kPa

MOISTURE AND ACID GAS FREE MEASURED CALCULATED 35.99

DETERMINED DEW POINT °C      VAPOUR PRESSURE PENTANES PLUS kPa: 0.

RELATIVE DENSITY: MOISTURE FREE AS SAMPLED MEASURED 0.711 CALCULATED 0.711      MOISTURE AND ACID GAS FREE MEASURED CALCULATED 0.573

PSEUDO CRITICAL PROPERTIES (CALCULATED): AS SAMPLED pPc(ads) 4996. kPa pTc 206.3 K      ACID GAS FREE pPc(ads) 4539. kPa pTc 187.4 K

H<sub>2</sub>S g/m<sup>3</sup> 23.82

RELATIVE MOLECULAR MASS TOTAL GAS 20.58      C<sub>7</sub> +

C<sub>5</sub> + ML/MOL 0.000

GROSS HEATING VALUE AS PER AGA REPORT #5 30.94 MJ/M<sup>3</sup> @ 15C AND 101.325 KPA



# ALTECH

BOX 1357, GRANDE PRAIRIE, AB T8V 4Z1

## ANALYSIS GAS ANALYSIS

24 HOUR ANSWERING SERVICE

(403) 532-5044

OR (403) 354-8312

GA 125

Lab. No.

Container Identity

Licence No.

COLUMBIA GAS DEVELOPMENT OF CANADA LTD.

Operator

CPA Number

I 48

Well Name

KB

GRD

-Elevations Meters-

ALTECH

Company

Field or Area

Pool or Zone

Name of Sampler

Test Recovery

Sampling Point

AMT & Type of Cushion

Mud Resistivity

Pumping

Flowing

Gas Lift

Swab

Water (M3/d)

Oil (M3/d)

Gas (M3/d)

Type of Production

Production Rates

Separator

Treater

As Received

Separator

Treater

As Received

Test Interval

From: \_\_\_\_\_

Gauge Pressure KPa

Temperature C

To: \_\_\_\_\_

23/8/91

23/8/91

BILL

Perforations

From: \_\_\_\_\_

Date Sampled

Date Received

Date Reported

Analyst

To: \_\_\_\_\_

Mole Fraction Air Free As Rec'd

Mole Fraction Air Free Acid Free

Liquid Volume mL/M3 As Rec'd

GROSS HEATING VALUE MJ/M3 @ 15 C & 101.325 KPa

30.69

36.34

Moisture Free As Sampled

Moisture & Acid Gas Free

RELATIVE DENSITY (Calculated)

air = 1 @ 15 C & 101.325 KPa

0.706

0.569

Moisture Free As Sampled

Moisture & Acid Gas Free

VAPOR PRESSURE PENTANES PLUS (Calculated)

KPa(abs) @ 40 C

0.0

PSUEDO CRITICAL PROPERTIES (Calculated)

As Sampled

Acid Gas Free

5075.7 KPa

208.7 K

4595.7 KPa

188.8

pPc

pTc

pPc

pTc

	Mole Fraction Air Free As Rec'd	Mole Fraction Air Free Acid Free	Liquid Volume mL/M3 As Rec'd
N2	0.0306	0.0362	
CO2	0.1258	0.0000	
H2S	0.0294	0.0000	
C1	0.8140	0.9637	
C2	0.0001	0.0001	
C3	0.0000	0.0000	0.0
C4	0.0000	0.0000	0.0
nC4	0.0000	0.0000	0.0
iC5	0.0000	0.0000	0.0
nC5	0.0000	0.0000	0.0
C6	0.0000	0.0000	0.0
C7+	0.0000	0.0000	0.0
C8			
C9			
C10			
C11			
C12			
TOTAL	1.0000	1.0000	0.0
