

018599

"*Rite in the Rain.*"

WATERPROOF
FIELD BOOK

No. 300

400
-600

19 Feb, 1968.

Attempt to pull the rods out.
Day Shift.

Work started at 2:15 P.M.

~~Work started at 2:15 P.M.~~

Site - A.T. 5.

90' rods left in the hole.

4:15 P.M. - Stopped work.

NO progress.

Last sample collected.

100 feet rods left:

As we were yesterday.

Rods left in hole - 90'.

26 Feb, 1968.

Survey work at carmacks -
to prepare contour map of
area containing coal seams.

SURVEYORS: - E. KIRPIAK
R. PATTERSON.

DEPARTED WHITEHORSE AT
10:45 A.M.

Reached carmacks at 1:30 P.M.

1 hr - Lunched arranging
accommodation

2:30 - Sub-soil field work.

Spent 3 hours in locating
posts & to have a birds eye
view of the area and to plan
the work.

Located - Survey post of
406 107 26 - found
at the extreme end of the
line cut.

- Post 4 of Ed Kirriak claim
is also found along blaze line.

406 107 26

155'

246'

27 Feb, 1968.

7.15 A.M. — down hotel.

French A.T. #1.

Asy — 145°

Dip — 57°

coal seams underlain by black M-
-mudstone and on the top is exposed
Congl. bed.


underlain by coarse S.St.

length of the coal seams exposed in
the main trench —

For 52' exposed coal seam in the trench is
quite pure and further down the
section until contact with S.St.
consists of small bands of S.St.

Bearing of glaze line close to

A.T. #1 — 82° .

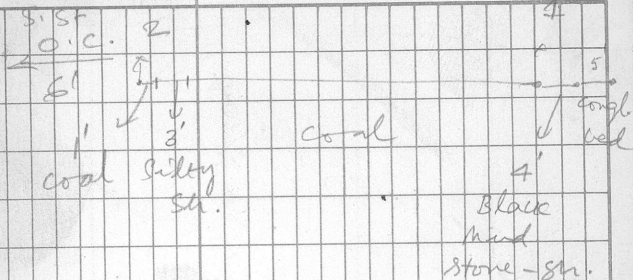

A.T. #2

5 & 6. Nothin out —
weps exposed.

Congl. float on the top of coal
seam

A.T. #3

7 & 8 — coal seam


A.T. #4

9 & 10. — coal seam

A. T # 5

Az - 165°

dip - 56°

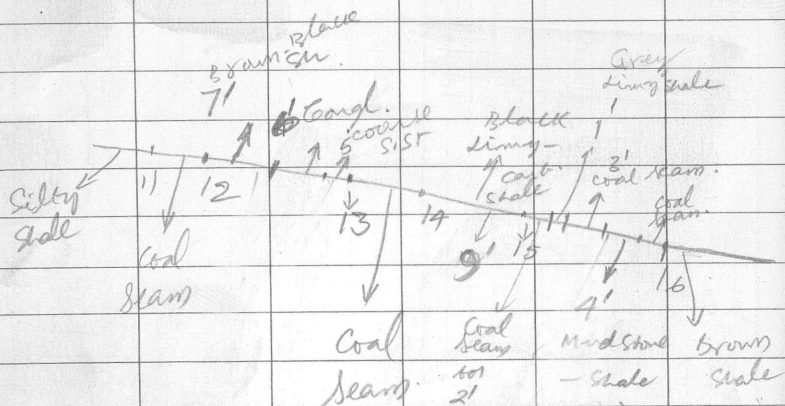

2 Posts

May 10/66

Post #1
Rod #2
1500'L
staked by W. R. Newman
Feb 24/66

Post #2
Rod #5
1500'L
W-Neely
Feb. 28/66



Scott #9

Post #1

1500L

1500 SW

April 24/66

J-ASP

~~Gray #2~~

\$ ↑ Post #1
Gray 15

S 30° E

Post #2

Gray 13

1500L

Gray Phillips

Feb. 12/66

#11

1500L

Scott #10

Post #1

April 24/66

1500R

1500 S.W.

J-ASP

~~Gray 16 #2~~

Post #1
Gray 16

Post #2

Gray 14

1500R

Gray Phillips

Feb. 12/66

#12

1500R
