DRILL HOLE DATA

15 + 25-7 | 13 + 23-4
13 + 11-7 | 9 + 16-14 | 7 + 12-6
7 + 10-10 | 3 + 16-10 | 1 + 15-7
1 + 4-17 | 2 + 14-10 | 6 + 17-9
6 + 14-3 | 8 + 35-8

DRIVING AND YARDAGE ESTIMATE

UNIT	AREA SQ. YDS.	Nº of POINTS	AVG DEPTH (Ft) MUCK	GRAVEL	B.R	TOTAL FOOTAGE	VOLUME CU. YDS.
7	17,685	725	15	8	23	16,675	147,375
8	20,622	845	12	6	18	15,120	137,980
9	18,095	742	12	10	22	16,324	144,760
10	17,065	699	16	12	28	19,572	170,650
11	18,095	742	8	10	18	13,356	120,635
12	17,622	722	13	10	23	16,606	146,850
13	18,095	745	9	10	19	14,098	126,665
14	18,536	760	10.5	8.5	19	14,440	129,752
TOTAL	145,813	5980				126,281	1,124,165

Probable driving rate per 10 hr shift	150' ft.
Probable driving season May 10th to Aug. 25th	108 days
Driving crew required	12
Driving order	

LEGEND

- Thawed this Season
- Boundary of Seasons Thaw
- Point in Ground
- Point Pulled
- Dredge Limit
- Top of Stripping Bank
- Power Line
- Creek
- Cross Section Line
- Co-ordinate Lines
- Claim Boundarys
- Pipe Line 1st pos.
- Pipe Line 2nd pos.
- 4 + 8-10 { Drill Hole Nº above. ft. of muck and D.S. to right

DRIVING AND YARDAGE DATA

BLOCK Nº	THAWING PERIOD: DATE STARTED	DATE TO B.R.	DATE COMPLETE	AREA 50 YARDS	LINEAL FT. OF POINTS DRIVEN	NUMBER OF POINTS	DEPTHS (FEET): MUCK	POINT	CUBIC YARDS: MUCK	DREDGING SECTION	TOTAL	PERCENT THAWED: AT BEGINNING SEASON	DURING SEASON	AT END OF SEASON	EQUIVALENT CUBIC YARDS: MUCK	DREDGING SECTION	TOTAL

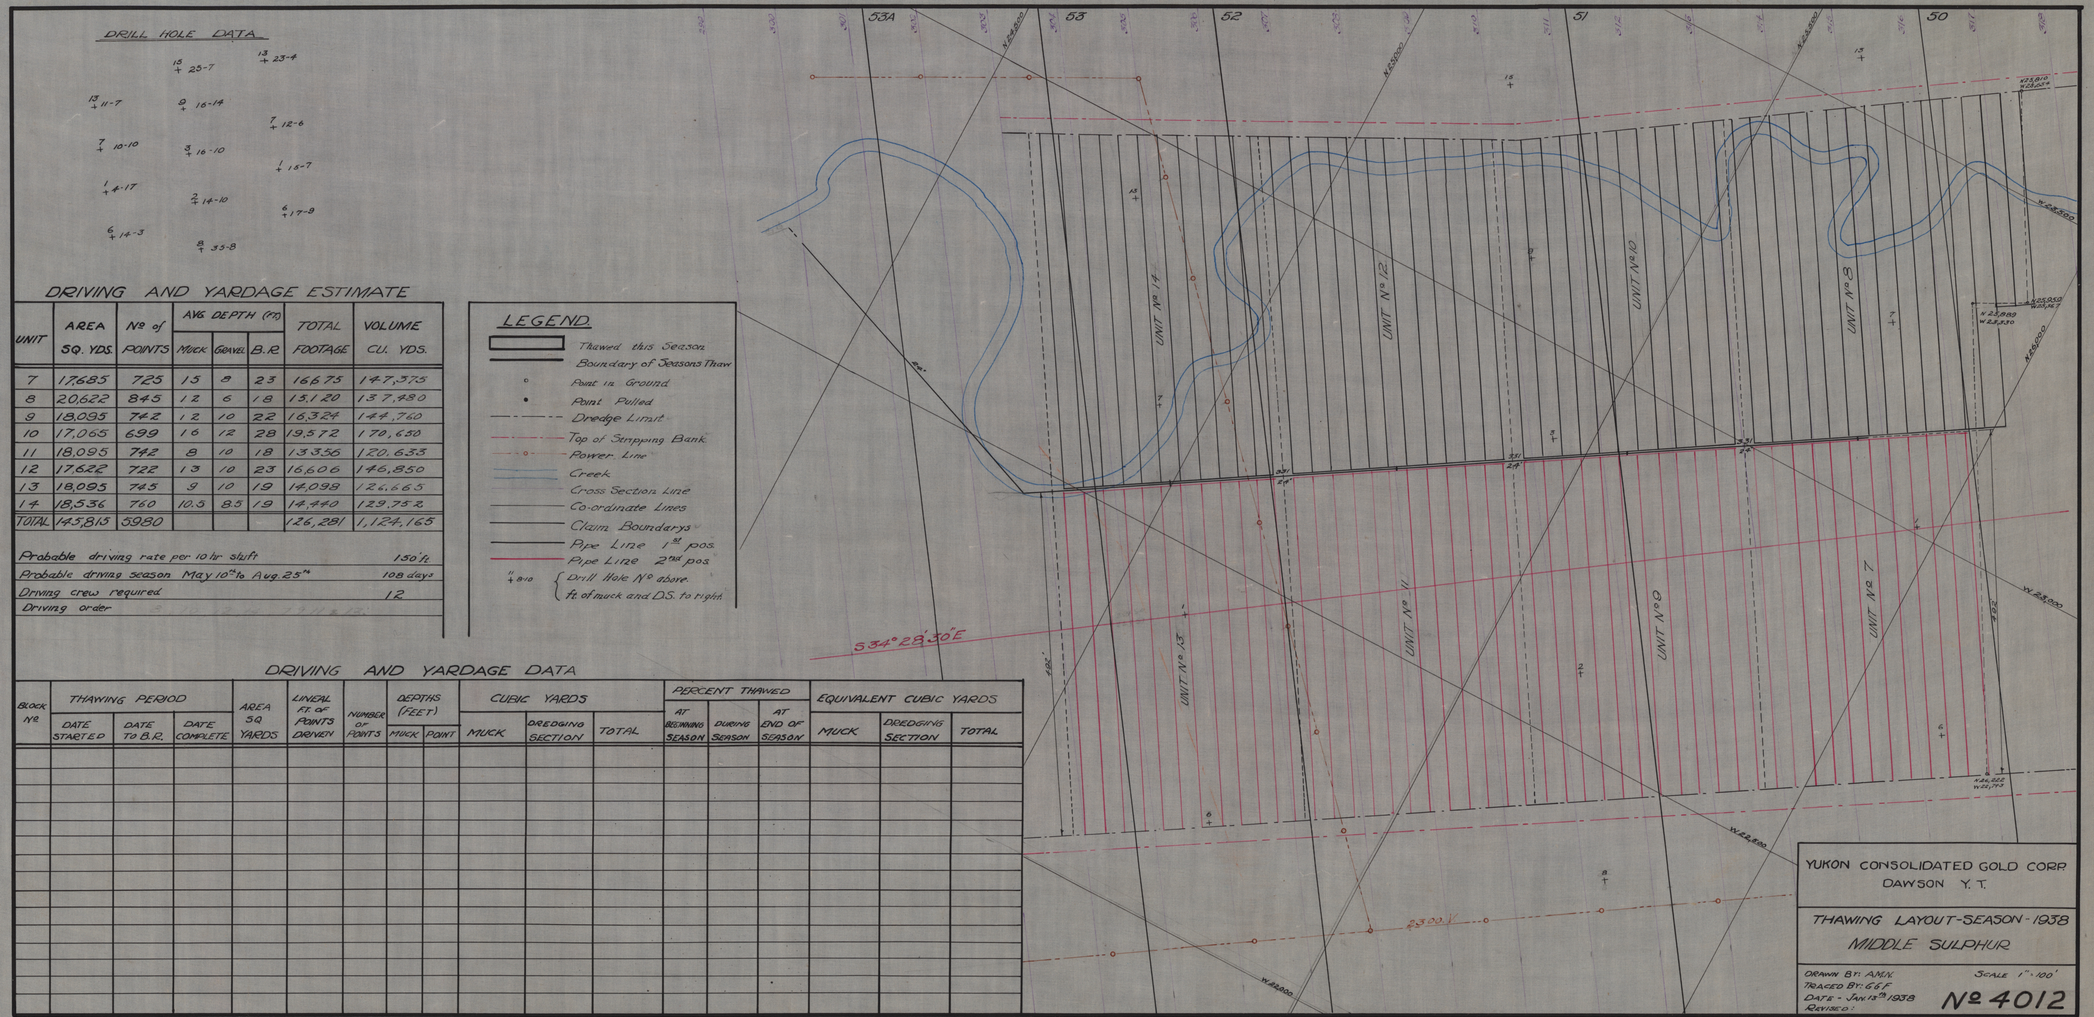

YUKON CONSOLIDATED GOLD CORP
DAWSON Y. T.

THAWING LAYOUT-SEASON-1938
MIDDLE SULPHUR

DRAWN BY: A.M.K.
TRACED BY: E.E.F.
DATE - JAN 13th 1938
REVISED:
SCALE 1" = 100'

Nº 4012

e011168542
YCGC26702
